


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	29, '14
1									M
2			Project Plan assumptions	303 days?	Tue 12/31/13	Fri 2/27/15			
3			Availability of SRM versions	303 days	Tue 12/31/13	Fri 2/27/15			
4	✓		SRM 3.0 SP2	0 days	Tue 12/31/13	Tue 12/31/13		EMC	
5	✓		SRM 3.5	0 days	Fri 6/13/14	Fri 6/13/14		EMC	
6	✓		SRM 3.5 SP1	0 days	Fri 9/5/14	Fri 9/5/14		EMC	
7			SRM 3.5 SP2	0 days	Wed 10/29/14	Wed 10/29/14		EMC	
8			SRM 4.0 "WINE release"	0 days	Wed 12/31/14	Wed 12/31/14		EMC	
9			SRM 4.X (next CR release)	0 days	Fri 2/27/15	Fri 2/27/15		EMC	
10			Discovery sessions						
11	✓		NAM - one discovery session per week	0 days	Mon 10/27/14	Mon 10/27/14		Citi	
12			EMEA - TBD					Citi	
13			APAC - TBD					Citi	
14			Other assumptions as of 10.27.2014	1 day?	Mon 10/27/14	Mon 10/27/14			
15	✓		No response received for the Final Requirements request due on 9.26.2014	0 days	Mon 10/27/14	Mon 10/27/14		Citi	
16	✓		No ViPR Controller requirements	0 days	Mon 10/27/14	Mon 10/27/14		Citi	
17	✓		All change requests approved in a timely manner	0 days	Mon 10/27/14	Mon 10/27/14		Citi	
18	✓		SRM discovery of NAM storage by the end of 2014 is not a priority	0 days	Mon 10/27/14	Mon 10/27/14		Citi	
19			<i>SAN Team to determine if ViPR SRM meets Global/NAM/EMEA/APAC requirements</i>					Al Mahmood	
20									
21			Architecture and Infrastructure Designs	227 days	Thu 1/16/14	Fri 11/28/14			
22	✓		Requirements collection	182 days	Thu 1/16/14	Fri 9/26/14			
23	✓		NAM region	159 days	Mon 2/3/14	Thu 9/11/14			

Project: SRM Deployment Project
Date: Mon 10/27/14

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	29, '1
24	✓		Sizing details collected	20 days	Mon 2/3/14	Fri 2/28/14			M
25	✓		Core Infrastructure Location agreed	20 days	Mon 2/3/14	Fri 2/28/14			
26	✓		Design received from EMC	5 days	Mon 3/3/14	Fri 3/7/14	24,25		
27	✓		Design reviewed with teams	1 day	Mon 3/10/14	Mon 3/10/14	26		
28	✓		Updated design received from EMC	4 days	Tue 3/11/14	Fri 3/14/14	27		
29	✓ 		Availability of ESX LVM capacity checked	10 days	Mon 3/10/14	Fri 3/21/14	26		
30	✓ 		Mgmt decision to go with physical servers	2 days	Mon 3/24/14	Tue 3/25/14	29		
31	✓		Updated design for SRM 3.5 SP1 received	1 day	Thu 9/11/14	Thu 9/11/14			
32	✓		EMEA region	129 days	Mon 3/17/14	Thu 9/11/14			
33	✓		Sizing details collected	27 days	Mon 3/17/14	Tue 4/22/14			
34	✓		Design received from EMC	15 days	Wed 4/23/14	Tue 5/13/14	33		
35	✓		Core Infrastructure Location agreed	5 days	Wed 5/14/14	Tue 5/20/14	34		
36	✓		Design reviewed with teams	5 days	Wed 5/14/14	Tue 5/20/14	34		
37	✓		Updated design received from EMC	5 days	Wed 5/21/14	Tue 5/27/14	36		
38	✓		Updated design for SRM 3.5 SP1 received	1 day	Thu 9/11/14	Thu 9/11/14			
39			APAC region	165.5 days	Mon 3/17/14	Mon 11/3/14			
40	✓		Sizing details collected	91 days	Mon 3/17/14	Mon 7/21/14			
41	✓		Design received from EMC	38 days	Tue 7/22/14	Thu 9/11/14	40		
42	✓		Design reviewed with teams	12 days	Fri 9/12/14	Mon 9/29/14	41		
43	✓ 		Core Infrastructure Location agreed	21 days	Fri 9/12/14	Fri 10/10/14	41		
44	✓ 		Updated design received from EMC	14.5 days	Tue 9/30/14	Mon 10/20/14	42		
45			Availability of VM capacity checked	10 days	Mon 10/20/14	Mon 11/3/14	44		
46			Global Roll-up infrastructure	43 days	Wed 10/1/14	Fri 11/28/14			
47			Design received from EMC	23 days	Wed 10/1/14	Fri 10/31/14			
48			Design reviewed	20 days	Mon 11/3/14	Fri 11/28/14	47		
49									

Project: SRM Deployment Project
Date: Mon 10/27/14

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	29, '1
50			CATE Certification	61 days	Fri 9/5/14	Fri 11/28/14			M
51			Certification of SRM 3.5 SP1	61 days	Fri 9/5/14	Fri 11/28/14	6		
52									
53			Deployment in NAM region	337 days?	Mon 3/17/14	Tue 6/30/15			
54	✓		Core Infrastructure Provisioning (MWDC & SWDC)	136 days	Mon 3/17/14	Mon 9/22/14			
55	✓		TCRS completed and submitted	11 days	Mon 3/17/14	Mon 3/31/14	28		
56	✓		TCRS approved and Apertures generated	7 days	Tue 4/1/14	Wed 4/9/14	55		
57	✓		NEMS IDs for EMC consultants created	22 days	Tue 4/1/14	Wed 4/30/14			
58	✓		SWDC	118 days	Thu 4/10/14	Mon 9/22/14			
59	✓		Core servers provisioned	17 days	Thu 4/10/14	Fri 5/2/14	56		
60	✓		Post-Build SA activities completed	5 days	Mon 5/5/14	Fri 5/9/14	59		
61	✓		Servers handed over to SRM Deployment Team	0 days	Mon 5/12/14	Mon 5/12/14	60		
62	✓		SRM 3.0 installed	6 days	Mon 5/12/14	Mon 5/19/14	61		
63	✓		SRM Deployment on HOLD (Java security issue)	14 days	Tue 5/27/14	Fri 6/13/14			
64	✓		SRM 3.5 installed	6 days	Mon 6/16/14	Mon 6/23/14	5,63		
65	✓		SRM upgraded to 3.5 SP1	3 days	Thu 9/18/14	Mon 9/22/14			
66	✓		MWDC	114 days	Thu 4/10/14	Tue 9/16/14			
67	✓		Core servers provisioned	18 days	Thu 4/10/14	Mon 5/5/14	56		
68	✓		Servers handed over to SRM Deployment Team	5 days	Tue 5/6/14	Mon 5/12/14	67		
69	✓		SRM 3.0 installed	5 days	Tue 5/20/14	Mon 5/26/14	68,62		
70	✓		SRM Deployment on HOLD (Java security issue)	14 days	Tue 5/27/14	Fri 6/13/14			
71	✓		SRM 3.5 installed	20 days	Mon 6/16/14	Fri 7/11/14	5,70		
72	✓		SRM upgraded to 3.5 SP1	3 days	Fri 9/12/14	Tue 9/16/14			
73			Collectors Provisioning	170 days?	Tue 4/1/14	Mon 11/24/14			
74			Sites connected to SWDC core infra	170 days	Tue 4/1/14	Mon 11/24/14			
75	✓		SWDC	0 days	Tue 9/30/14	Tue 9/30/14			

Project: SRM Deployment Project
Date: Mon 10/27/14

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	29, '14	M
76	✓		GTDC	125 days	Tue 4/1/14	Mon 9/22/14				
77	✓		TCRS for VMs	11 days	Tue 4/1/14	Tue 4/15/14				
78	✓		CMP for servers on DEV cloud	5 days	Wed 4/16/14	Tue 4/22/14	77			
79	✓		SRM 3.0 installed	8 days	Mon 5/12/14	Wed 5/21/14	61			
80	✓		SRM 3.5 installed	6 days	Mon 6/16/14	Mon 6/23/14	5,61,70			
81	✓		SRM 3.5 upgraded to SP1	6 days	Mon 9/15/14	Mon 9/22/14				
82			Mexico (Jardines, QRDC, Monterrey)	31 days	Mon 10/13/14	Mon 11/24/14				
83	✓		TCRS for VMs completed and submitted	1 day	Mon 10/13/14	Mon 10/13/14				
84			TCRS for VMs approved and Apertures generated	14 days	Tue 10/14/14	Fri 10/31/14	83			
85			VMs provisioned	5 days	Mon 11/3/14	Fri 11/7/14	84			
86			SRM 3.5 SP1 installed	11 days	Mon 11/10/14	Mon 11/24/14	85			
87			Jacsonville	31 days	Mon 10/13/14	Mon 11/24/14				
88	✓		TCRS for VMs completed and submitted	1 day	Mon 10/13/14	Mon 10/13/14				
89			TCRS for VMs approved and Apertures generated	14 days	Tue 10/14/14	Fri 10/31/14	88			
90			VMs provisioned	5 days	Mon 11/3/14	Fri 11/7/14	89			
91			SRM 3.5 SP1 installed	11 days	Mon 11/10/14	Mon 11/24/14	90			
92			Sites connected to MWDC core infra	24 days?	Tue 9/30/14	Fri 10/31/14				
93	✓		MWDC	0 days	Tue 9/30/14	Tue 9/30/14				
94	✓		390G	0 days	Tue 9/30/14	Tue 9/30/14				
95	✓		Rutherford	0 days	Tue 9/30/14	Tue 9/30/14				
96			Ofallon	15 days?	Mon 10/13/14	Fri 10/31/14				
97	✓		TCRS for VMs completed and submitted	1 day	Mon 10/13/14	Mon 10/13/14				
98			TCRS for VMs approved and Apertures generated	14 days	Tue 10/14/14	Fri 10/31/14	97			
99			VMs provisioned							
100			SRM 3.5 SP1 installed							

Project: SRM Deployment Project
Date: Mon 10/27/14

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	29, '14	M
101			SAN Devices Discovery and Data Collection (arrays/switches/vCenter)	172 days	Fri 7/11/14	Mon 3/9/15				
102			Sites connected to SWDC core infra	172 days	Fri 7/11/14	Mon 3/9/15				
103			GTDC (1st area of collection)	7 days	Fri 7/11/14	Mon 7/21/14				
104			GTDC on HOLD (CISCO issue)	13 days	Tue 7/22/14	Thu 8/7/14	103			
105			GTDC continued	52 days	Fri 8/8/14	Mon 10/20/14	104			
106			SWDC	97 days	Fri 10/24/14	Mon 3/9/15				
107			QRDC	97 days	Fri 10/24/14	Mon 3/9/15				
108			Jardines	97 days	Fri 10/24/14	Mon 3/9/15				
109			Monterrey	97 days	Fri 10/24/14	Mon 3/9/15				
110			Jacksonville	97 days	Fri 10/24/14	Mon 3/9/15				
111			Sites connected to MWDC core infra	112 days	Fri 10/3/14	Mon 3/9/15				
112			390G	22 days	Fri 10/3/14	Mon 11/3/14				
113			MWDC	97 days	Fri 10/24/14	Mon 3/9/15				
114			Rutherford	32 days	Fri 10/17/14	Mon 12/1/14				
115			Ofallon	97 days	Fri 10/24/14	Mon 3/9/15				
116			Discovery activities (once a week, weekends only)	97 days	Fri 10/24/14	Mon 3/9/15				
117			weekend Oct.25-26.2014	2 days	Fri 10/24/14	Mon 10/27/14				
118			weekend Nov.01-02.2014	2 days	Fri 10/31/14	Mon 11/3/14				
119			weekend Nov.08-09.2014	2 days	Fri 11/7/14	Mon 11/10/14				
120			weekend Nov.15-16.2014	2 days	Fri 11/14/14	Mon 11/17/14				
121			weekend Nov.22-23.2014	2 days	Fri 11/21/14	Mon 11/24/14				
122			weekend Dec.06-07.2014	2 days	Fri 12/5/14	Mon 12/8/14				
123			weekend Jan.24-25.2015	2 days	Fri 1/23/15	Mon 1/26/15				
124			weekend Jan.31-Feb.01.2015	2 days	Fri 1/30/15	Mon 2/2/15				
125			weekend Feb.07-08.2015	2 days	Fri 2/6/15	Mon 2/9/15				

Project: SRM Deployment Project
Date: Mon 10/27/14

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	29, '15
126			weekend Feb.14-15.2015	2 days	Fri 2/13/15	Mon 2/16/15			
127			weekend Feb.21-22.2015	2 days	Fri 2/20/15	Mon 2/23/15			
128			weekend Feb.28-Mar.01.2015	2 days	Fri 2/27/15	Mon 3/2/15			
129			weekend Mar.07-08.2015	2 days	Fri 3/6/15	Mon 3/9/15			
130			Other activities related to SRM infrastructure	85 days?	Mon 11/24/14	Fri 3/20/15			
131			Install and configure UAT environment	10 days	Mon 12/8/14	Fri 12/19/14			
132			Upgrade ViPR SRM 3.5.1 to SP2	3 days	Mon 11/24/14	Wed 11/26/14			
133			Upgrade ViPR SRM to "WINE" release	10 days	Mon 1/5/15	Fri 1/16/15			
134			Upgrade ViPR SRM to next ("CR") release	10 days	Mon 3/9/15	Fri 3/20/15			
135			SRM Infrastructure stress test (at SRM 3.5 SPX infra)						
136			Operational activities	205 days?	Wed 9/17/14	Tue 6/30/15			
137			DEMO sessions	15 days?	Wed 9/17/14	Tue 10/7/14			
138			1st DEMO session	1 day	Wed 9/17/14	Wed 9/17/14			
139			2nd DEMO session	1 day	Tue 10/7/14	Tue 10/7/14			
140			3rd DEMO session						
141			SRM Resource Consumption	28 days	Wed 9/24/14	Fri 10/31/14			
142			SRM consumption document received from EMC	1 day	Wed 9/24/14	Wed 9/24/14			
143			Document reviewed with the teams	1 day	Fri 9/26/14	Fri 9/26/14			
144			Resource consumption FE testing	5 days	Mon 10/6/14	Fri 10/10/14			
145			Updated document received from EMC	1 day	Tue 10/14/14	Tue 10/14/14			
146			Updated document reviewed by CATE	13 days	Wed 10/15/14	Fri 10/31/14	145		
147			Operational Run-Books	109 days	Mon 12/1/14	Thu 4/30/15			
148			Run-book writing with regulars reviews with Citi	99 days	Mon 12/1/14	Thu 4/16/15			
149			Run-book finalized and delivered to Citi	10 days	Fri 4/17/15	Thu 4/30/15	148		
150			Documentation and Knowledge Transfer	43 days	Fri 5/1/15	Tue 6/30/15	147		
151			Read-Only SRM IDs for CATE						

Project: SRM Deployment Project
Date: Mon 10/27/14

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	29, '11
152									M
153			Global Roll-up Infrastructure						
154			Infrastructure servers provisioning					Citi	
155			Install and configure ViPR SRM infrastrcuture servers for global roll-up	2 wks				EMC	
156									
157			Deployment in EMEA region	133.5 days?	Wed 5/28/14	Mon 12/1/14			
158			Core Infrastructure Provisioning (RDC)	115 days	Wed 5/28/14	Tue 11/4/14			
159			TCRS completed and submitted	71 days	Wed 5/28/14	Wed 9/3/14	37		
160			TCRS approved and Apertures generated	10 days	Thu 9/4/14	Wed 9/17/14	159		
161			Core Servers provisioned in RDC	22.5 days	Thu 9/18/14	Mon 10/20/14	160		
162			Post-Build SA activities completed	1 day	Mon 10/20/14	Tue 10/21/14	161		
163			Servers handed over to SRM Deployment Team	0.5 days	Tue 10/21/14	Tue 10/21/14	162		
164			CMP requests for access to servers by SRM Team	10 days	Wed 10/22/14	Tue 11/4/14	163		
165			ViPR SRM infrastrcuture servers installed and configured	1 wk					
166			Collectors Provisioning	45.5 days?	Mon 9/29/14	Mon 12/1/14			
167			Collectors in RDC & CGC	45.5 days	Mon 9/29/14	Mon 12/1/14			
168			TCRS for VMs completed and submitted	15.5 days	Mon 9/29/14	Mon 10/20/14		Citi	
169			TCRS for VMs approved and Apertures generated	10 days	Mon 10/20/14	Mon 11/3/14	168	Citi	
170			VMs provisioned	20 days	Mon 11/3/14	Mon 12/1/14	169	Citi	
171			Collectors in FDC	20 days	Fri 10/17/14	Thu 11/13/14			
172			TCRS for VMs completed and submitted	0.8 days	Thu 10/23/14	Thu 10/23/14		Citi	
173			TCRS for VMs approved and Apertures generated	11 days	Thu 10/23/14	Fri 11/7/14	172	Citi	
174			VMs provisioned	20 days	Fri 10/17/14	Thu 11/13/14		Citi	
175			Collectors in other sites	1 day?	Fri 10/17/14	Fri 10/17/14			

Project: SRM Deployment Project
Date: Mon 10/27/14

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	29, '1	M
176			TCRS for VMs completed and submitted					Citi		
177			TCRS for VMs approved and Apertures generated					Citi		
178			VMs provisioned					Citi		
179			All collectors provisioned and handed over to SRM Deployment Team					Citi		
180			SRM installation and configuration on collectors	1 wk				EMC		
181			SAN Devices Discovery and Data Collection(arrays/switches/vCenter) in EMEA							
182			Discovery activities (schedule to be determined)	6 wks				EMC		
183										
184			Deployment in APAC region							
185			Core Infrastructure Provisioning (Singapore)							
186			TCRS completed and submitted					Citi		
187			TCRS approved and Apertures generated					Citi		
188			Core Servers provisioned in Singapore					Citi		
189			Post-Build SA activities completed					Citi		
190			Servers handed over to SRM Deployment Team					Citi		
191			CMP requests for access to servers by SRM Team					Citi		
192			ViPR SRM infrastructure servers installed and configured	1 wk				EMC		
193			Collectors Provisioning							
194			All collectors provisioned and handed over to SRM Deployment Team					Citi		
195			SRM installation and configuration on collectors	2 wks				EMC		
196			SAN Devices Discovery and Data Collection(arrays/switches/vCenter) in APAC							

Project: SRM Deployment Project
Date: Mon 10/27/14

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	29, '1	M	
197			Discovery activities (schedule to be determined)	9 wks				EMC			
198											
199			Project Closure	22 days	Mon 6/1/15	Tue 6/30/15					

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	



Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

'13					Jan 5, '14							Jan 12, '14							Jan 19, '14							Jan 26, '14							Feb 2, '14							Feb 9, '14			
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T								

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

'13					Jan 5, '14							Jan 12, '14							Jan 19, '14							Jan 26, '14							Feb 2, '14							Feb 9, '14			
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T								

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

'13					Jan 5, '14							Jan 12, '14							Jan 19, '14							Jan 26, '14							Feb 2, '14							Feb 9, '14						
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T											

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

'13					Jan 5, '14							Jan 12, '14							Jan 19, '14							Jan 26, '14							Feb 2, '14							Feb 9, '14			
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T								

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

'13					Jan 5, '14							Jan 12, '14							Jan 19, '14							Jan 26, '14							Feb 2, '14							Feb 9, '14			
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T								

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

'13					Jan 5, '14							Jan 12, '14							Jan 19, '14							Jan 26, '14							Feb 2, '14							Feb 9, '14						
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T											

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


Deadline

Progress

'13					Jan 5, '14								Jan 12, '14								Jan 19, '14								Jan 26, '14								Feb 2, '14								Feb 9, '14			
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T													



Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

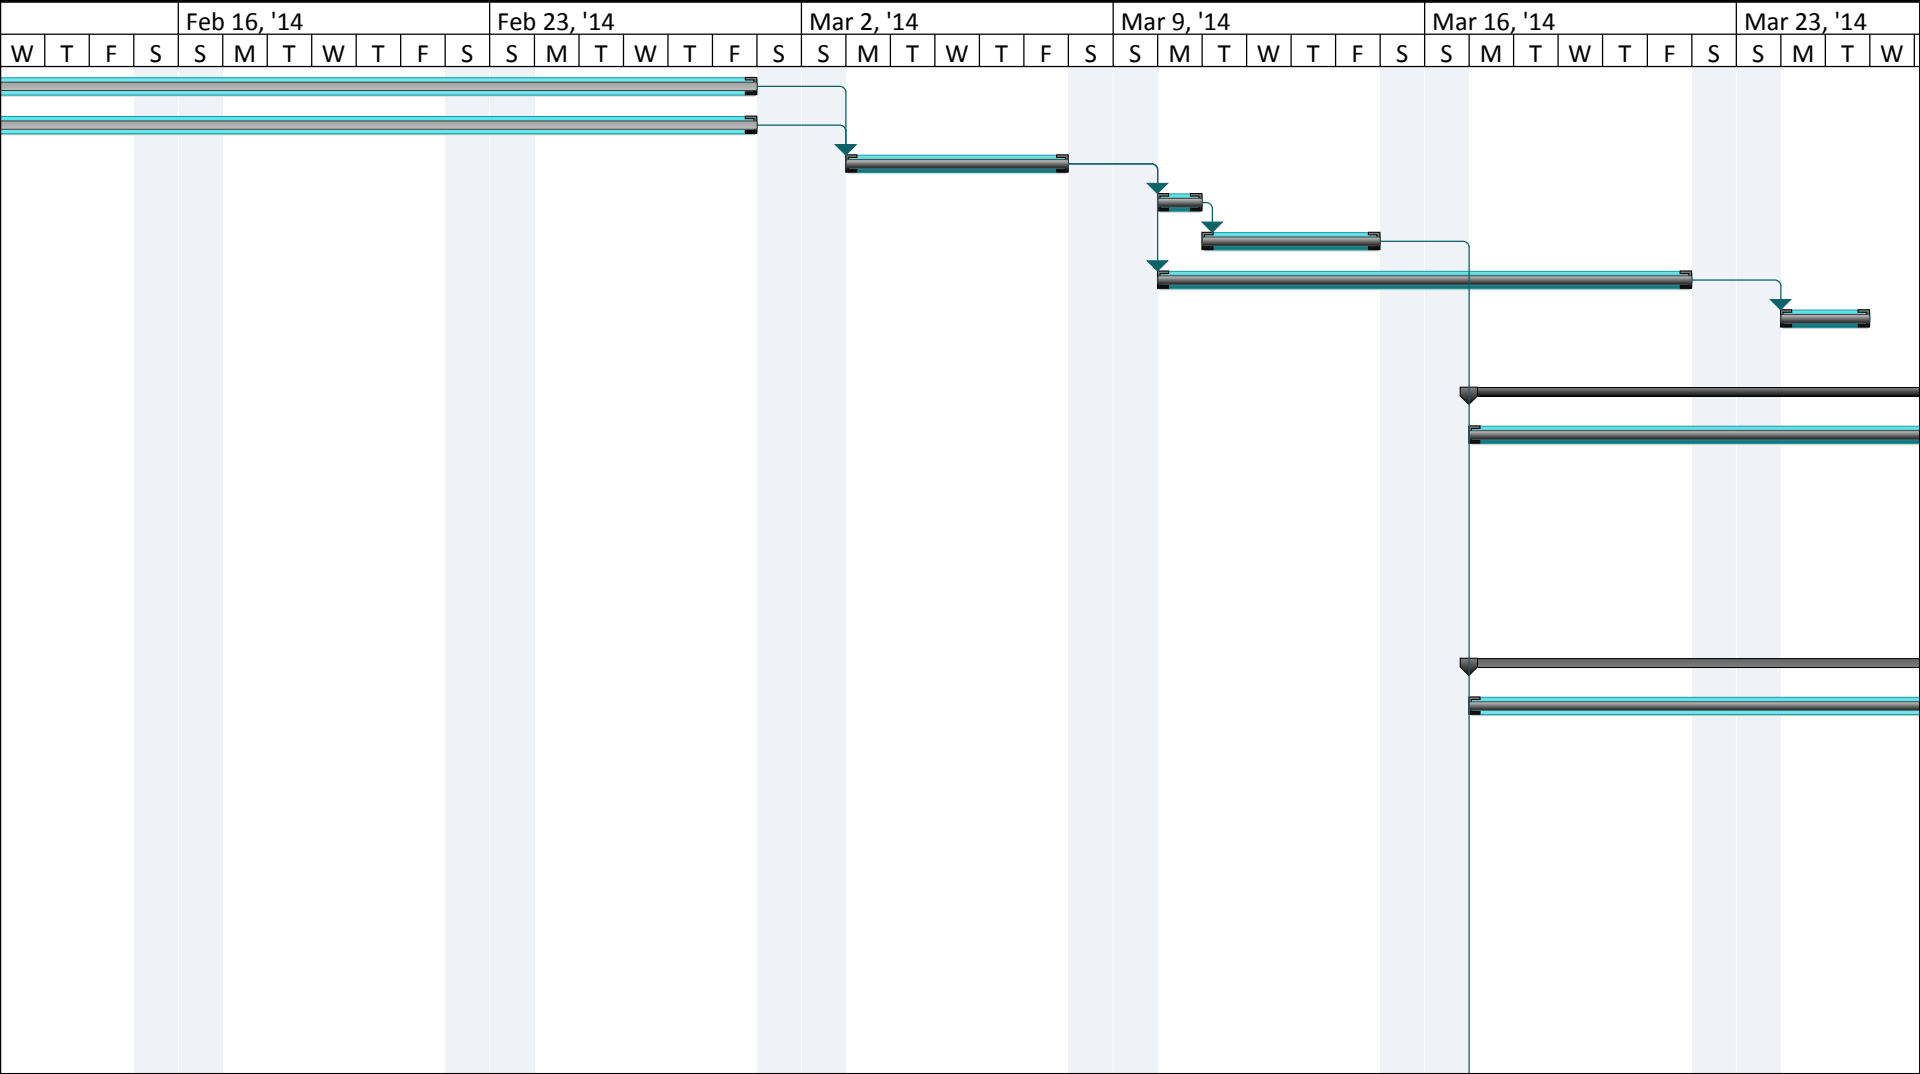

Project: SRM Deployment Project
Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only

Deadline

Progress

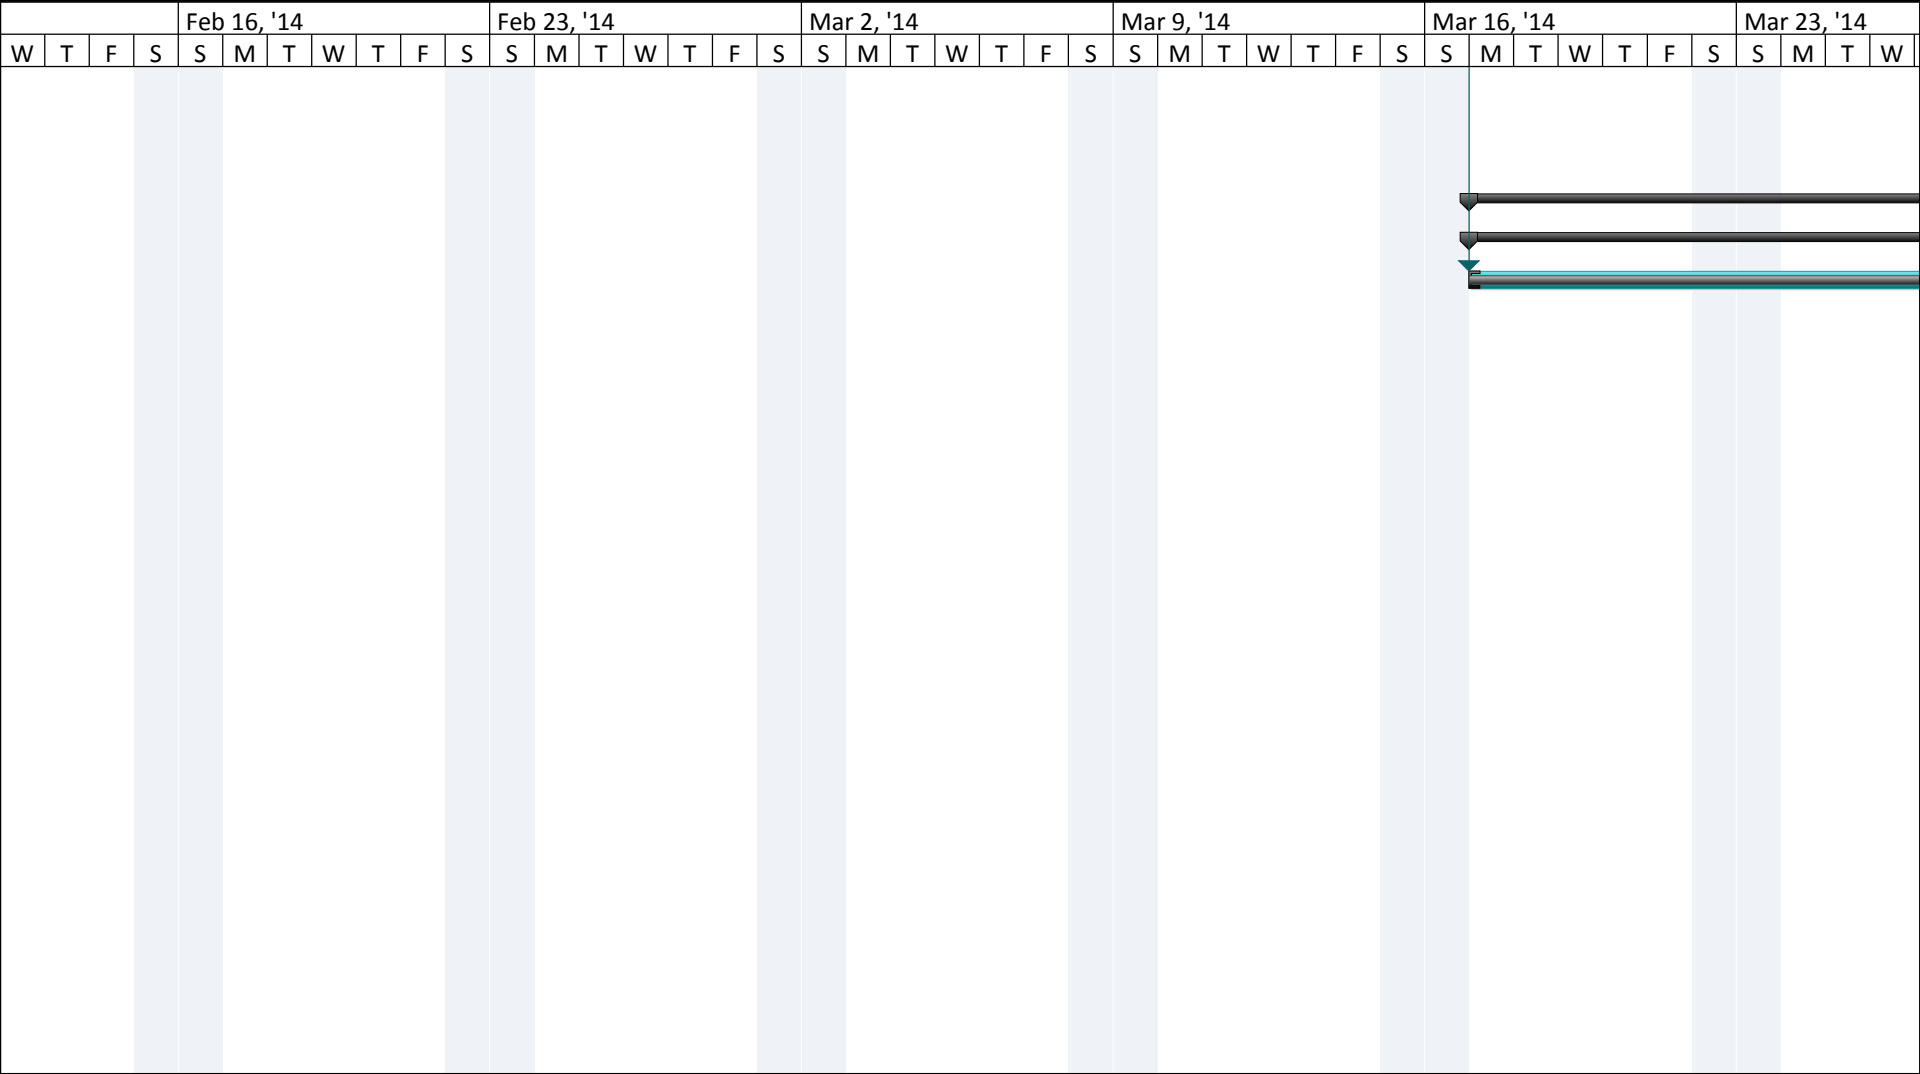

Project: SRM Deployment Project
Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

[illegible]

[illegible]

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

				Feb 16, '14								Feb 23, '14								Mar 2, '14								Mar 9, '14								Mar 16, '14								Mar 23, '14							
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W																

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

				Feb 16, '14								Feb 23, '14								Mar 2, '14								Mar 9, '14								Mar 16, '14								Mar 23, '14							
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W																

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

				Feb 16, '14				Feb 23, '14				Mar 2, '14				Mar 9, '14				Mar 16, '14				Mar 23, '14				
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


Deadline

Progress

				Feb 16, '14								Feb 23, '14								Mar 2, '14								Mar 9, '14								Mar 16, '14								Mar 23, '14			
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W												



Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

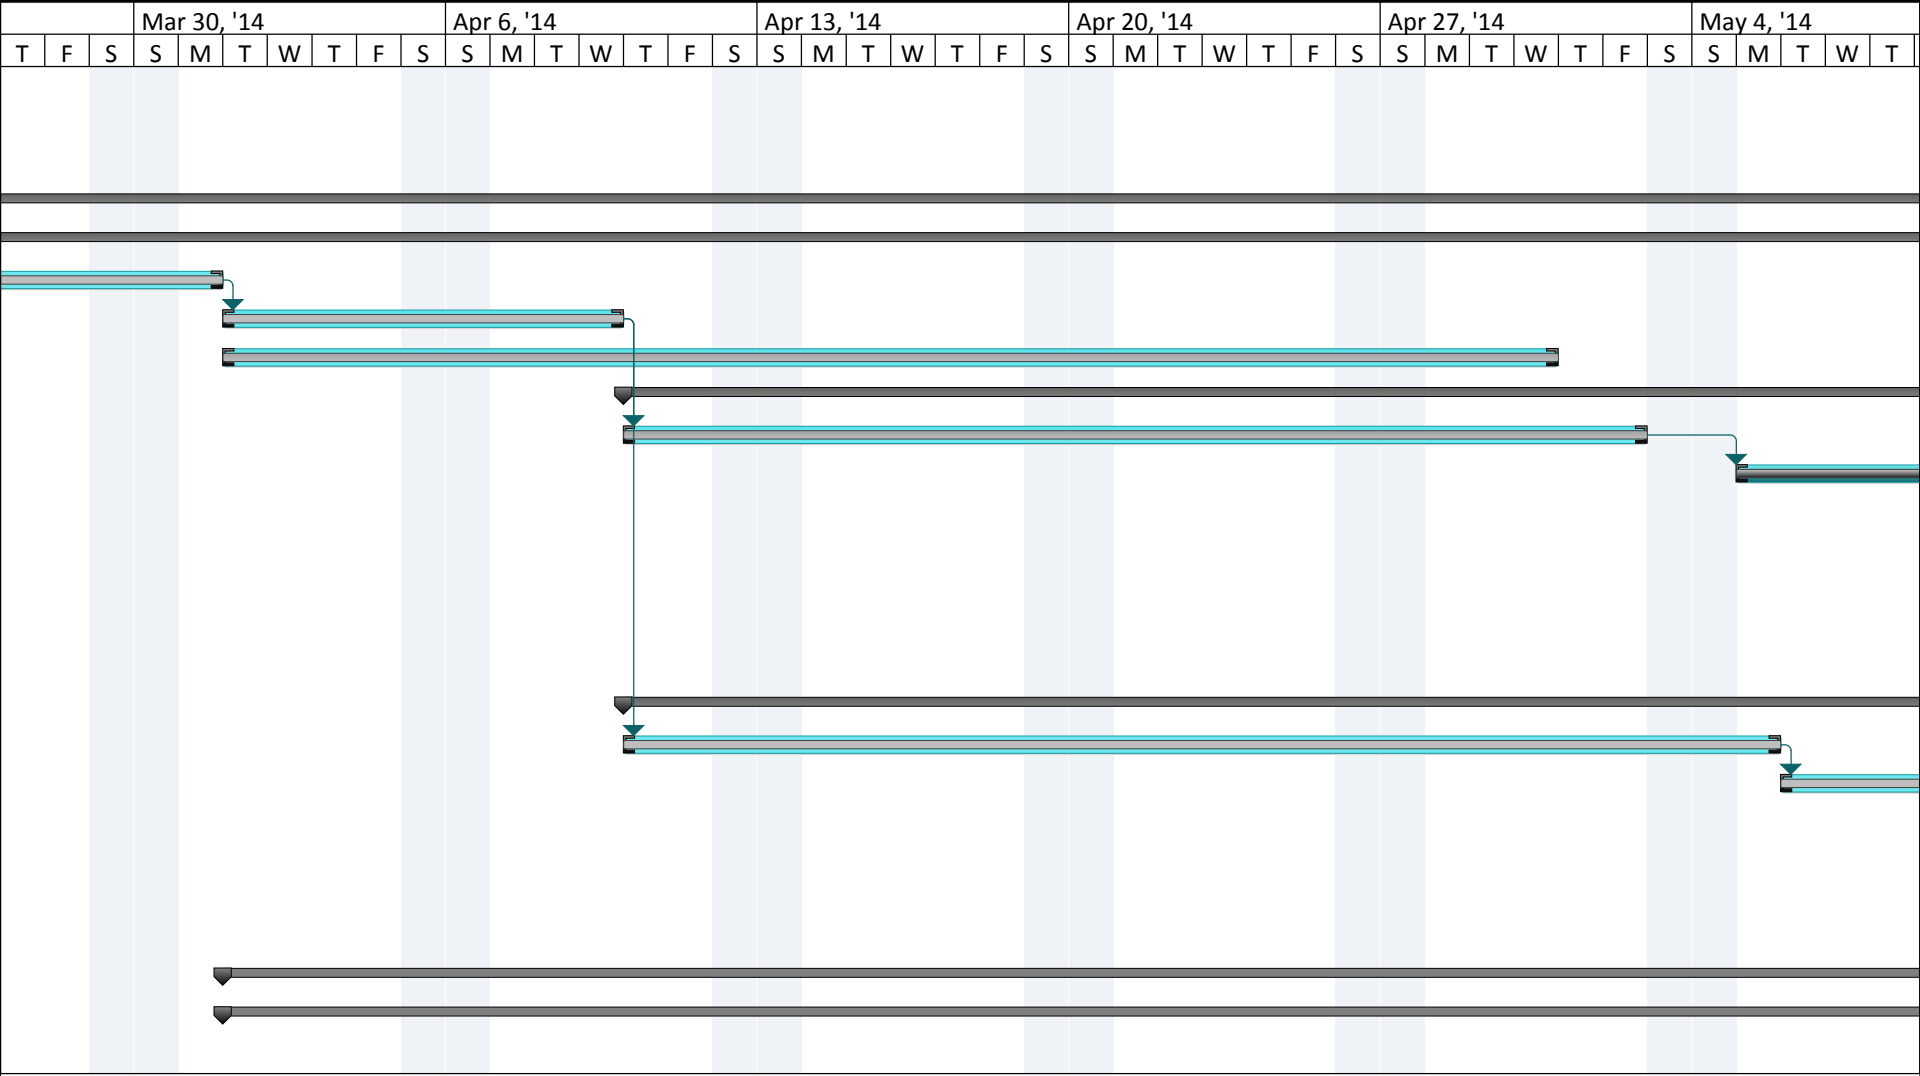

Project: SRM Deployment Project
Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only

Deadline

Progress

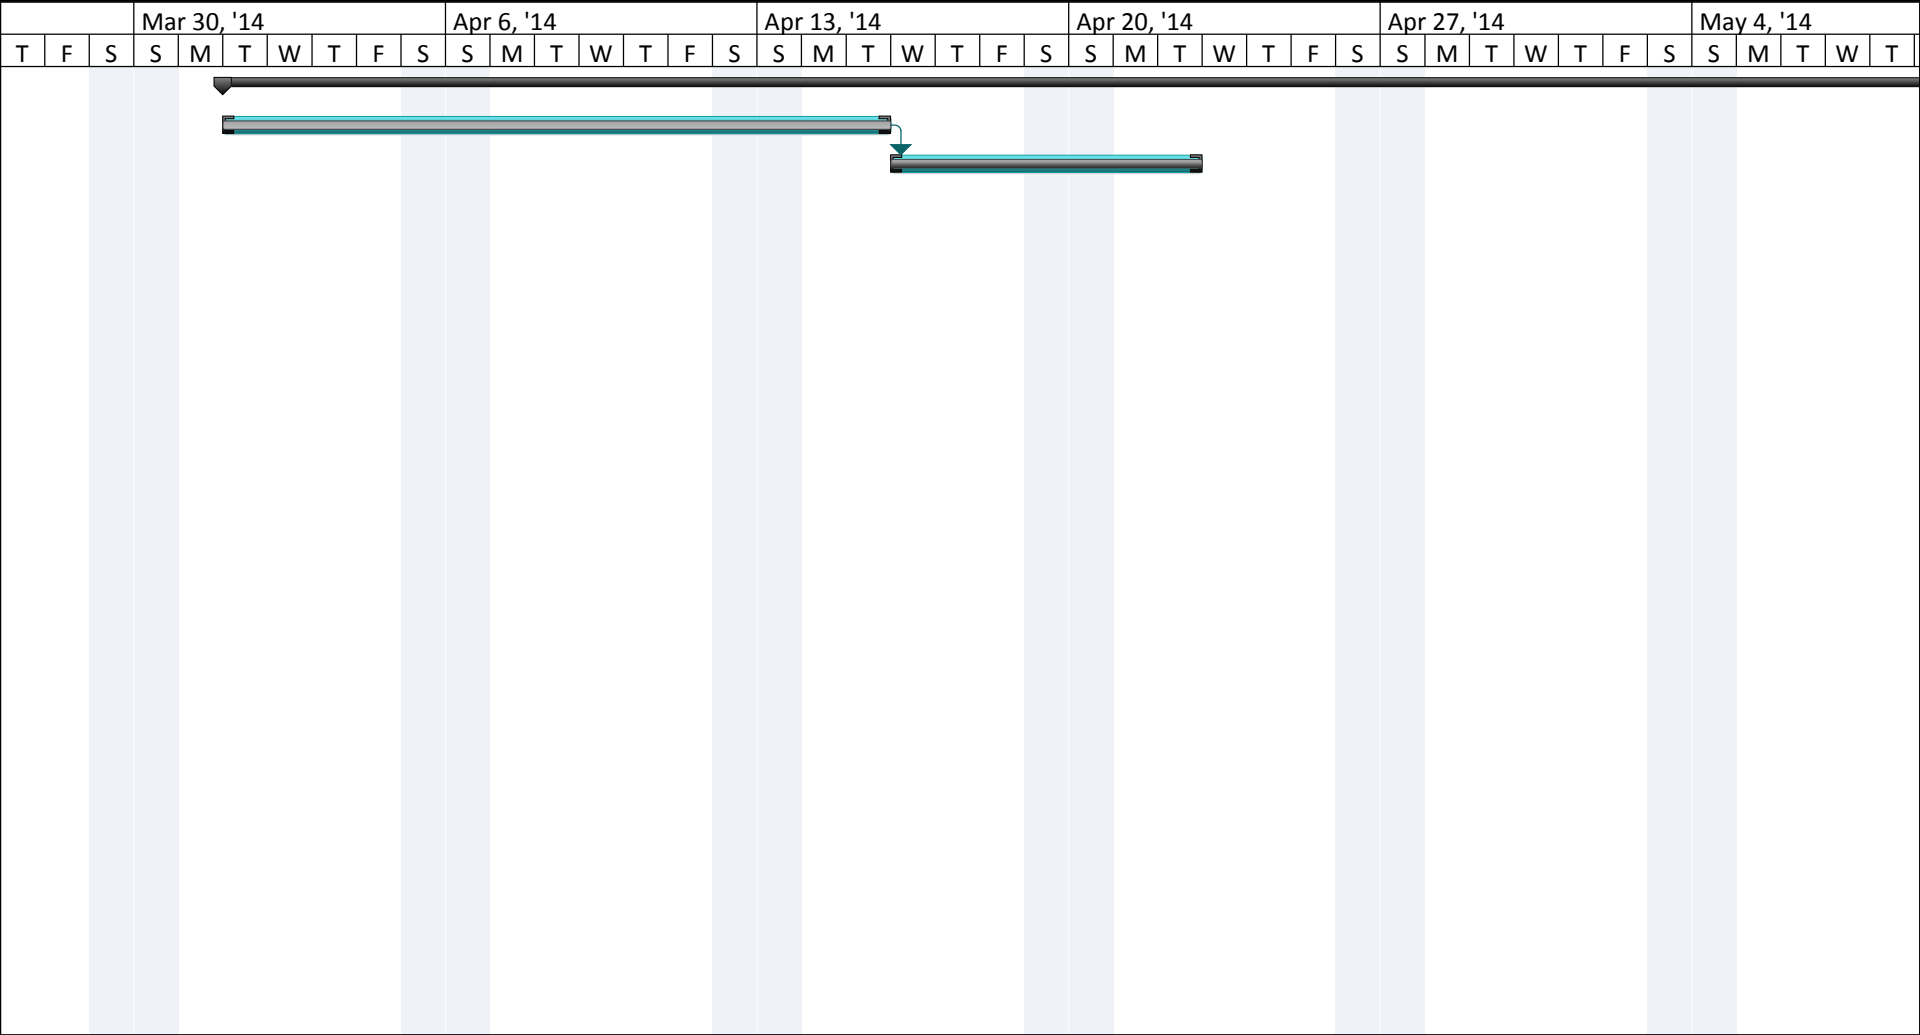

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

			Mar 30, '14							Apr 6, '14							Apr 13, '14							Apr 20, '14							Apr 27, '14							May 4, '14				
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T							

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

			Mar 30, '14							Apr 6, '14							Apr 13, '14							Apr 20, '14							Apr 27, '14							May 4, '14				
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T							

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

			Mar 30, '14							Apr 6, '14							Apr 13, '14							Apr 20, '14							Apr 27, '14							May 4, '14				
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T							

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

			Mar 30, '14							Apr 6, '14							Apr 13, '14							Apr 20, '14							Apr 27, '14							May 4, '14						
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T									

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

			Mar 30, '14							Apr 6, '14							Apr 13, '14							Apr 20, '14							Apr 27, '14							May 4, '14				
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T							



Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]

		May 11, '14								May 18, '14							May 25, '14							Jun 1, '14							Jun 8, '14							Jun 15, '14					
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]

		May 11, '14							May 18, '14							May 25, '14							Jun 1, '14							Jun 8, '14							Jun 15, '14						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

		May 11, '14							May 18, '14							May 25, '14							Jun 1, '14							Jun 8, '14							Jun 15, '14						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress


		May 11, '14								May 18, '14								May 25, '14								Jun 1, '14								Jun 8, '14								Jun 15, '14							
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F							

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

Jun 22, '14								Jun 29, '14								Jul 6, '14								Jul 13, '14								Jul 20, '14								Jul 27, '14							
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S					
<																																															

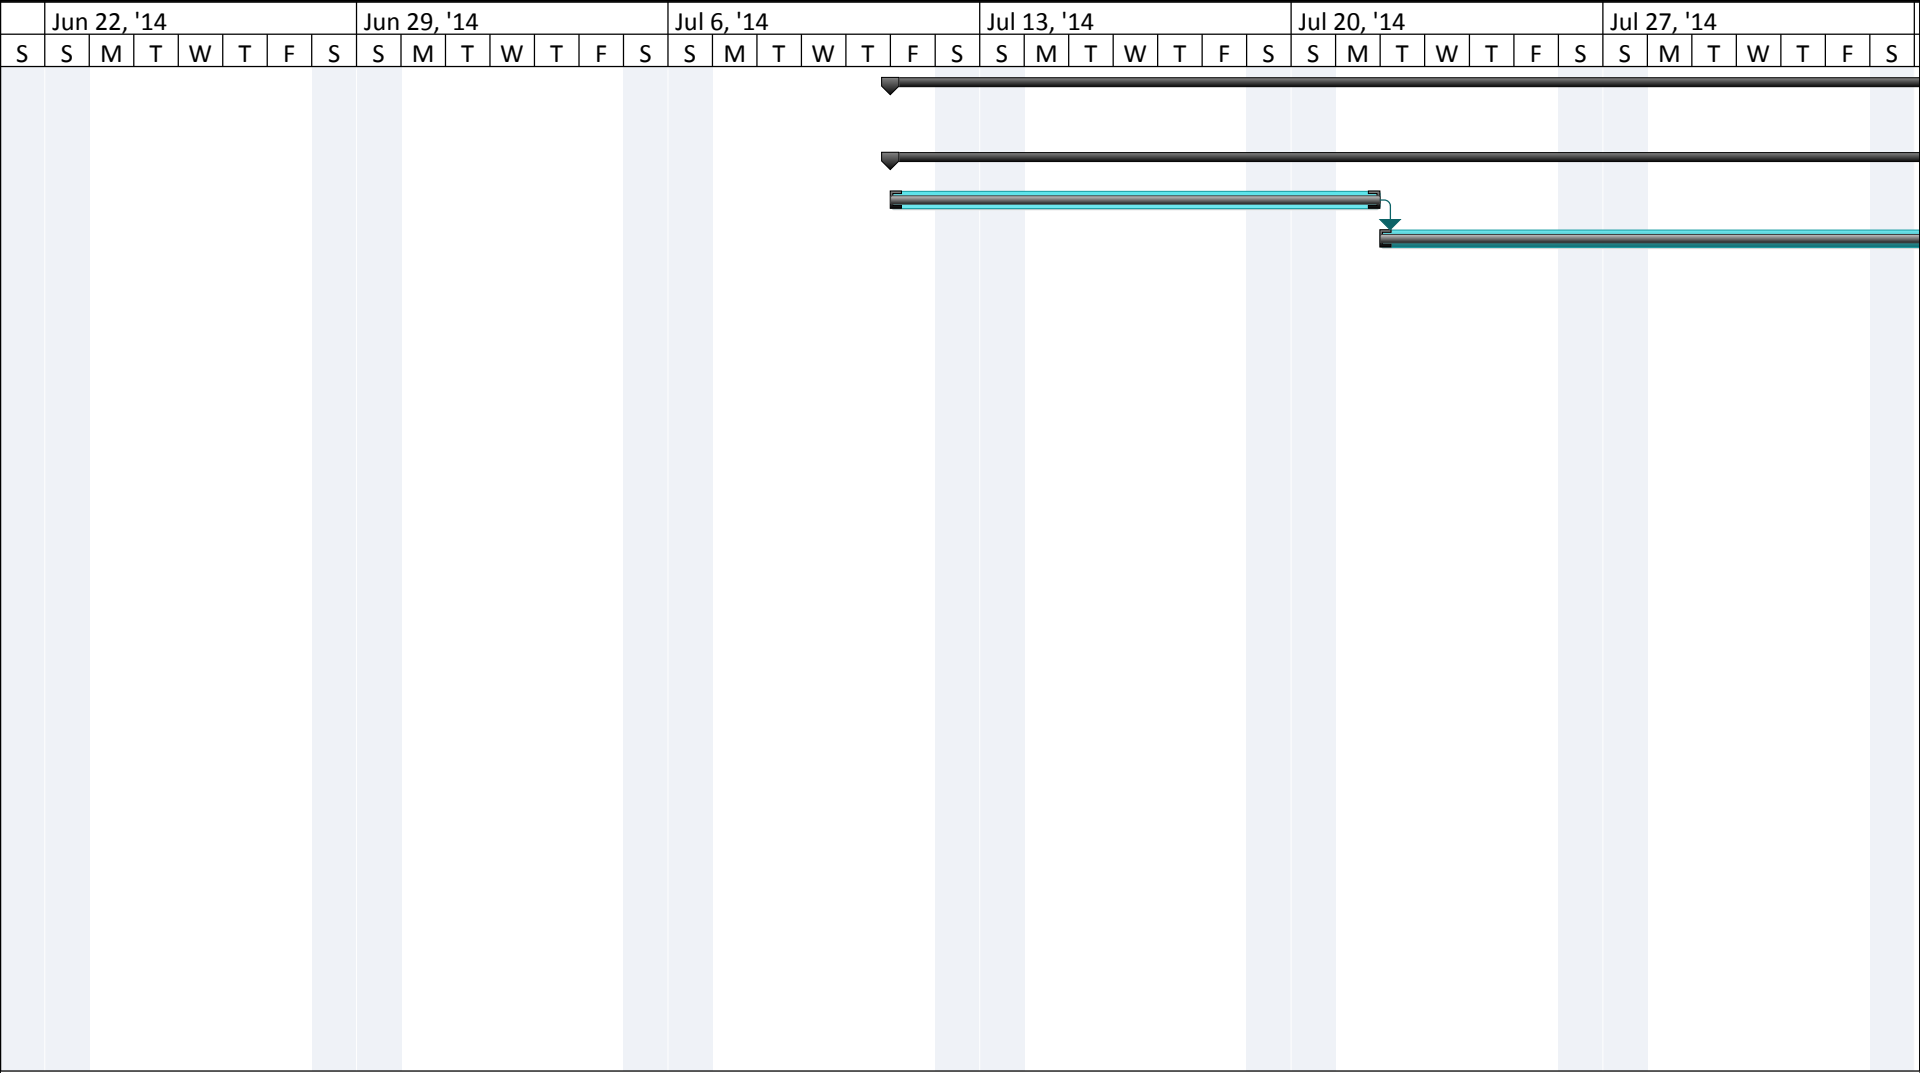

Project: SRM Deployment Project
Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


Deadline

Progress

Jun 22, '14								Jun 29, '14								Jul 6, '14								Jul 13, '14								Jul 20, '14								Jul 27, '14							
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S					



Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

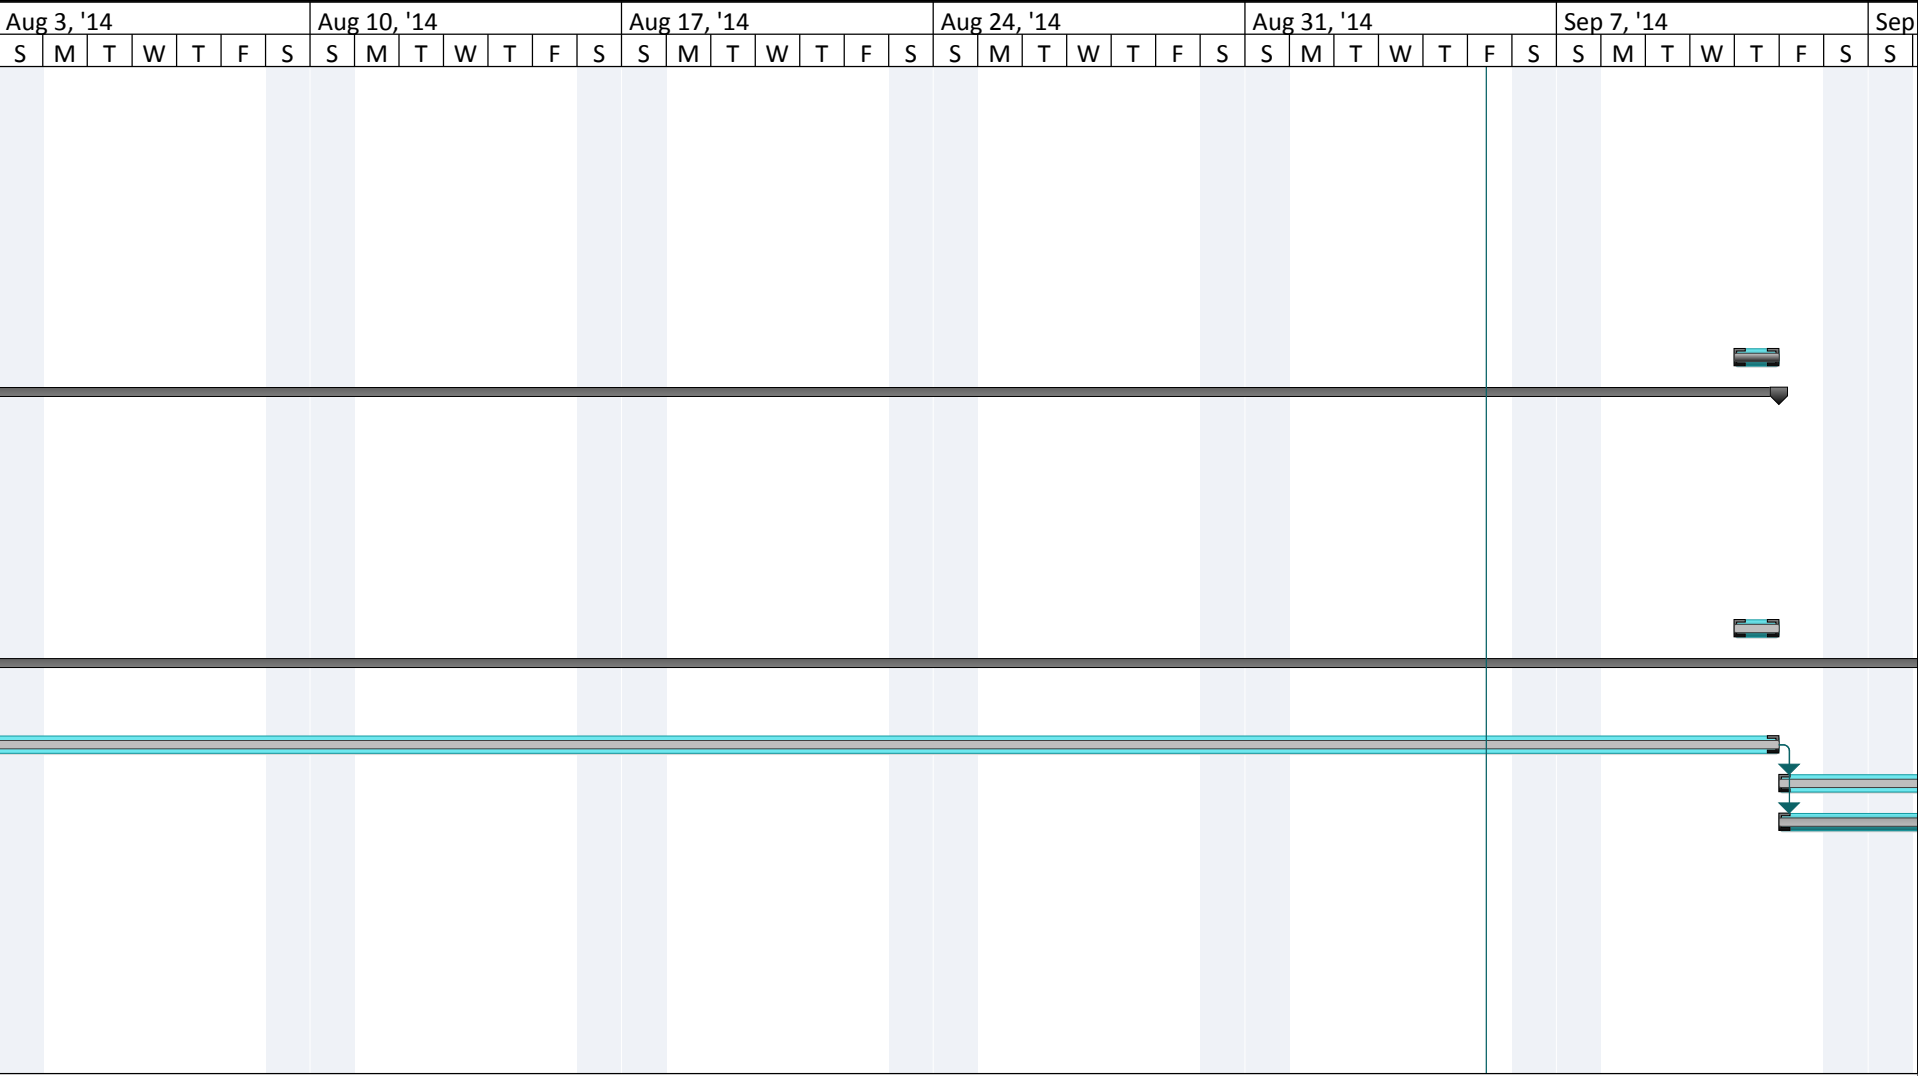

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

Aug 3, '14

S

M

T

W

T

F

S

Aug 10, '14

S

M

T

W

T

F

S

Aug 17, '14

S

M

T

W

T

F

S

Aug 24, '14

S

M

T

W

T

F

S

Aug 31, '14

S

M

T

W

T

F

S

Sep 7, '14

S

M

T

W

T

F

S

Sep

S

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline


Progress

Page 58

Aug 3, '14							Aug 10, '14							Aug 17, '14							Aug 24, '14							Aug 31, '14							Sep 7, '14							Sep
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S							



Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

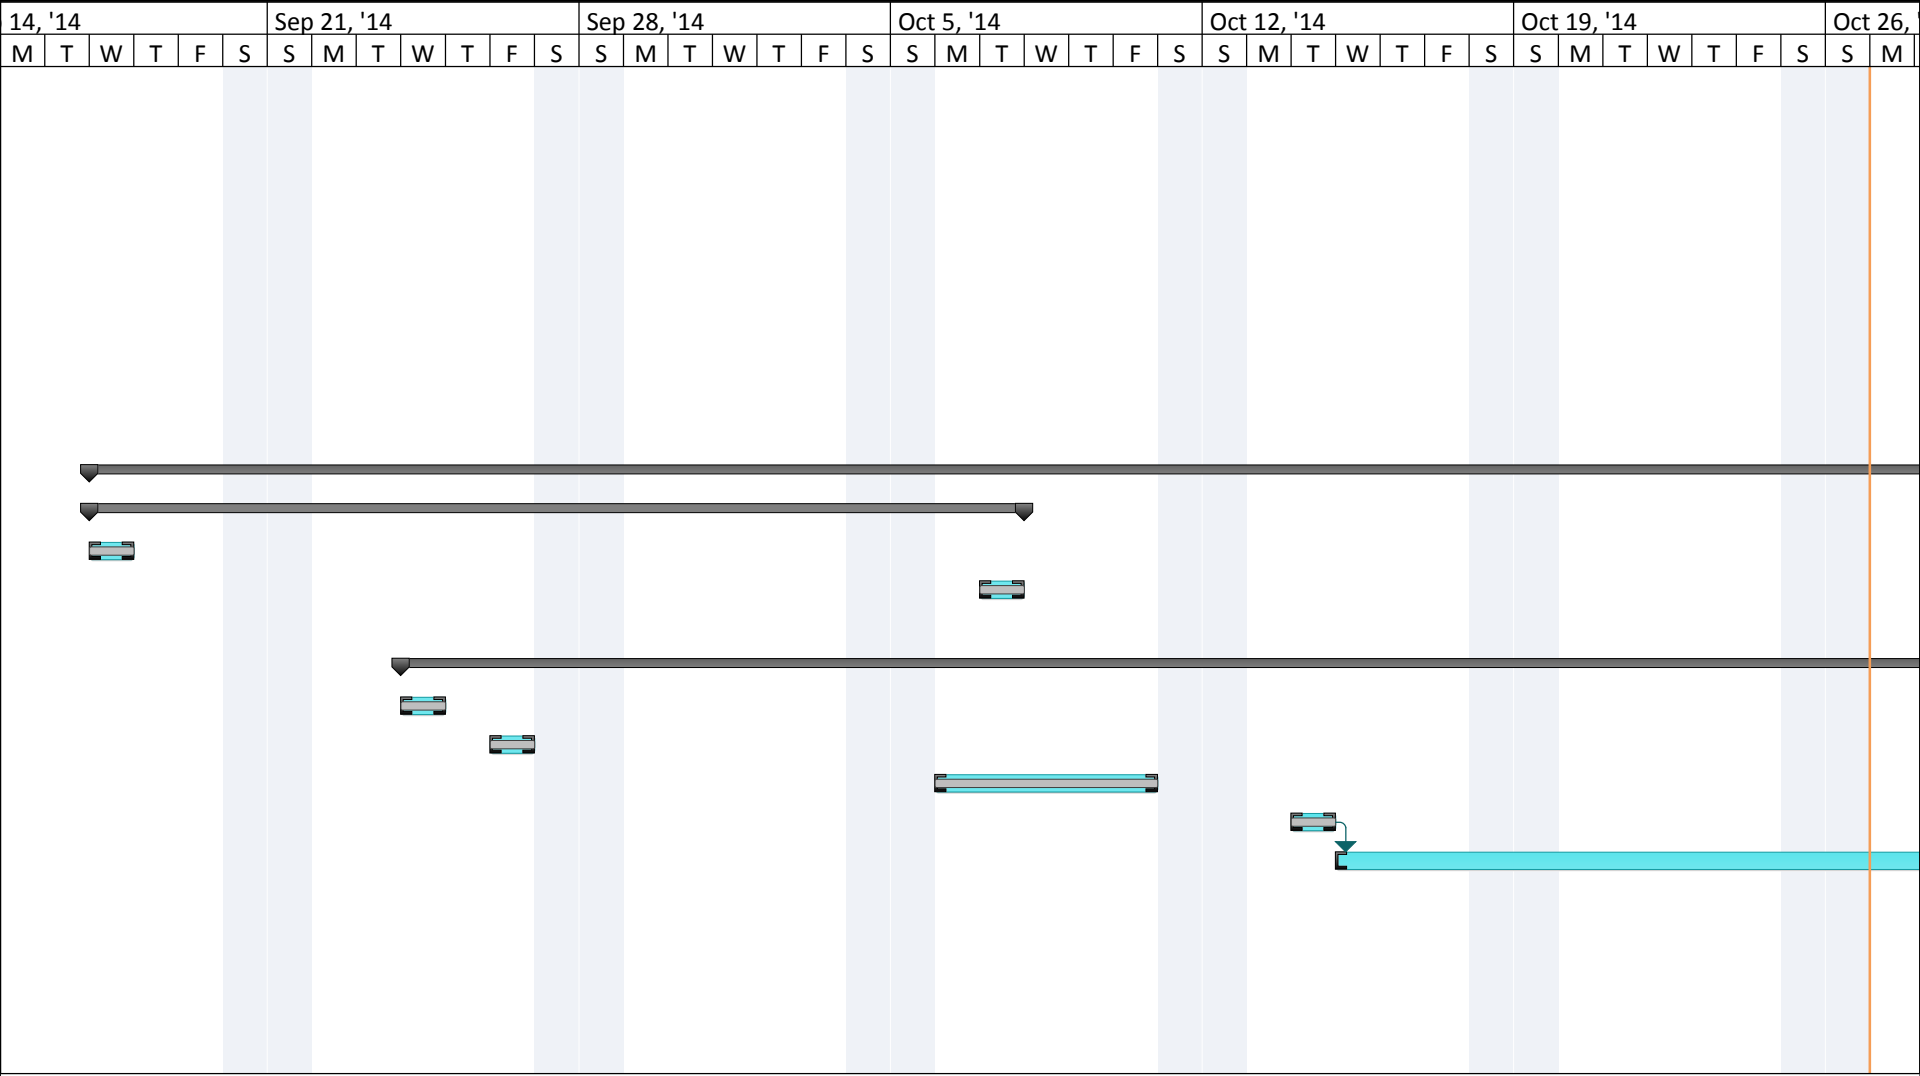

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	


[illegible]

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

14, '14						Sep 21, '14						Sep 28, '14						Oct 5, '14						Oct 12, '14						Oct 19, '14						Oct 26,	
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M		




Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

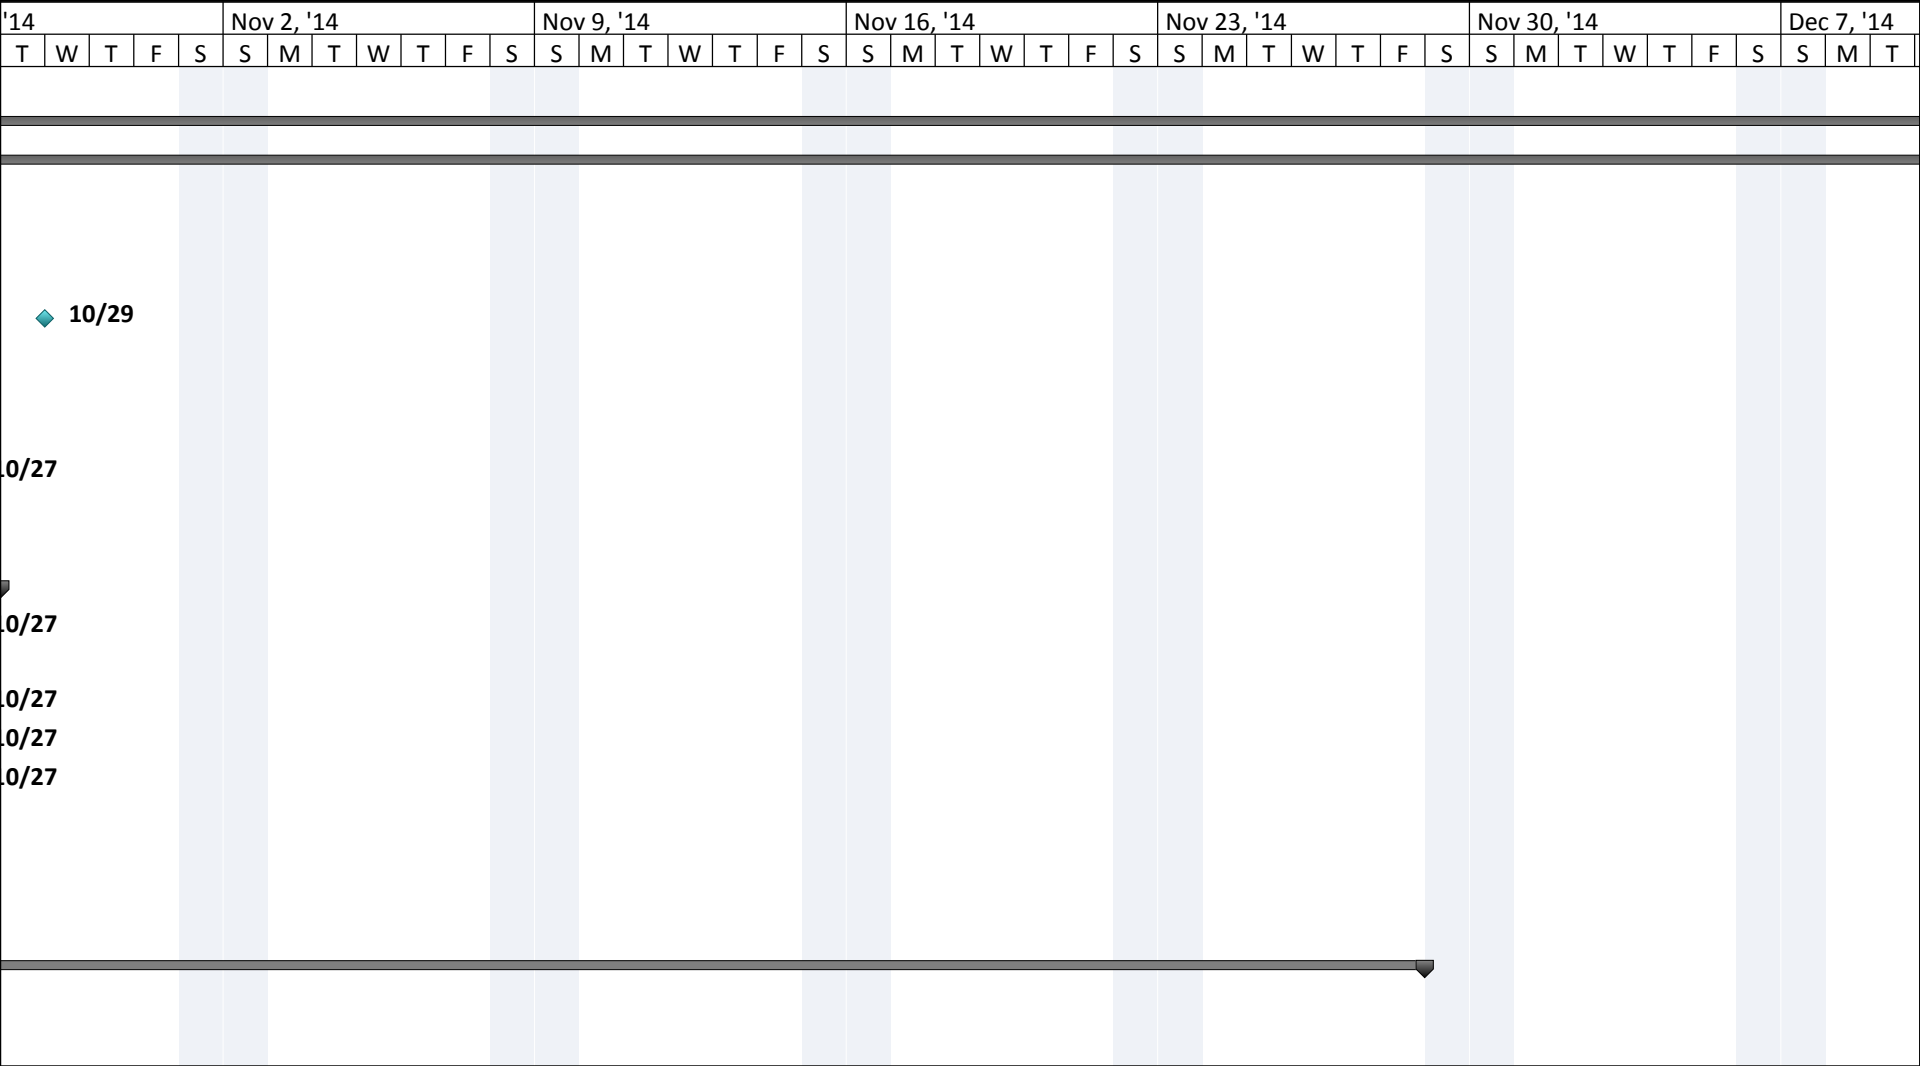


Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]

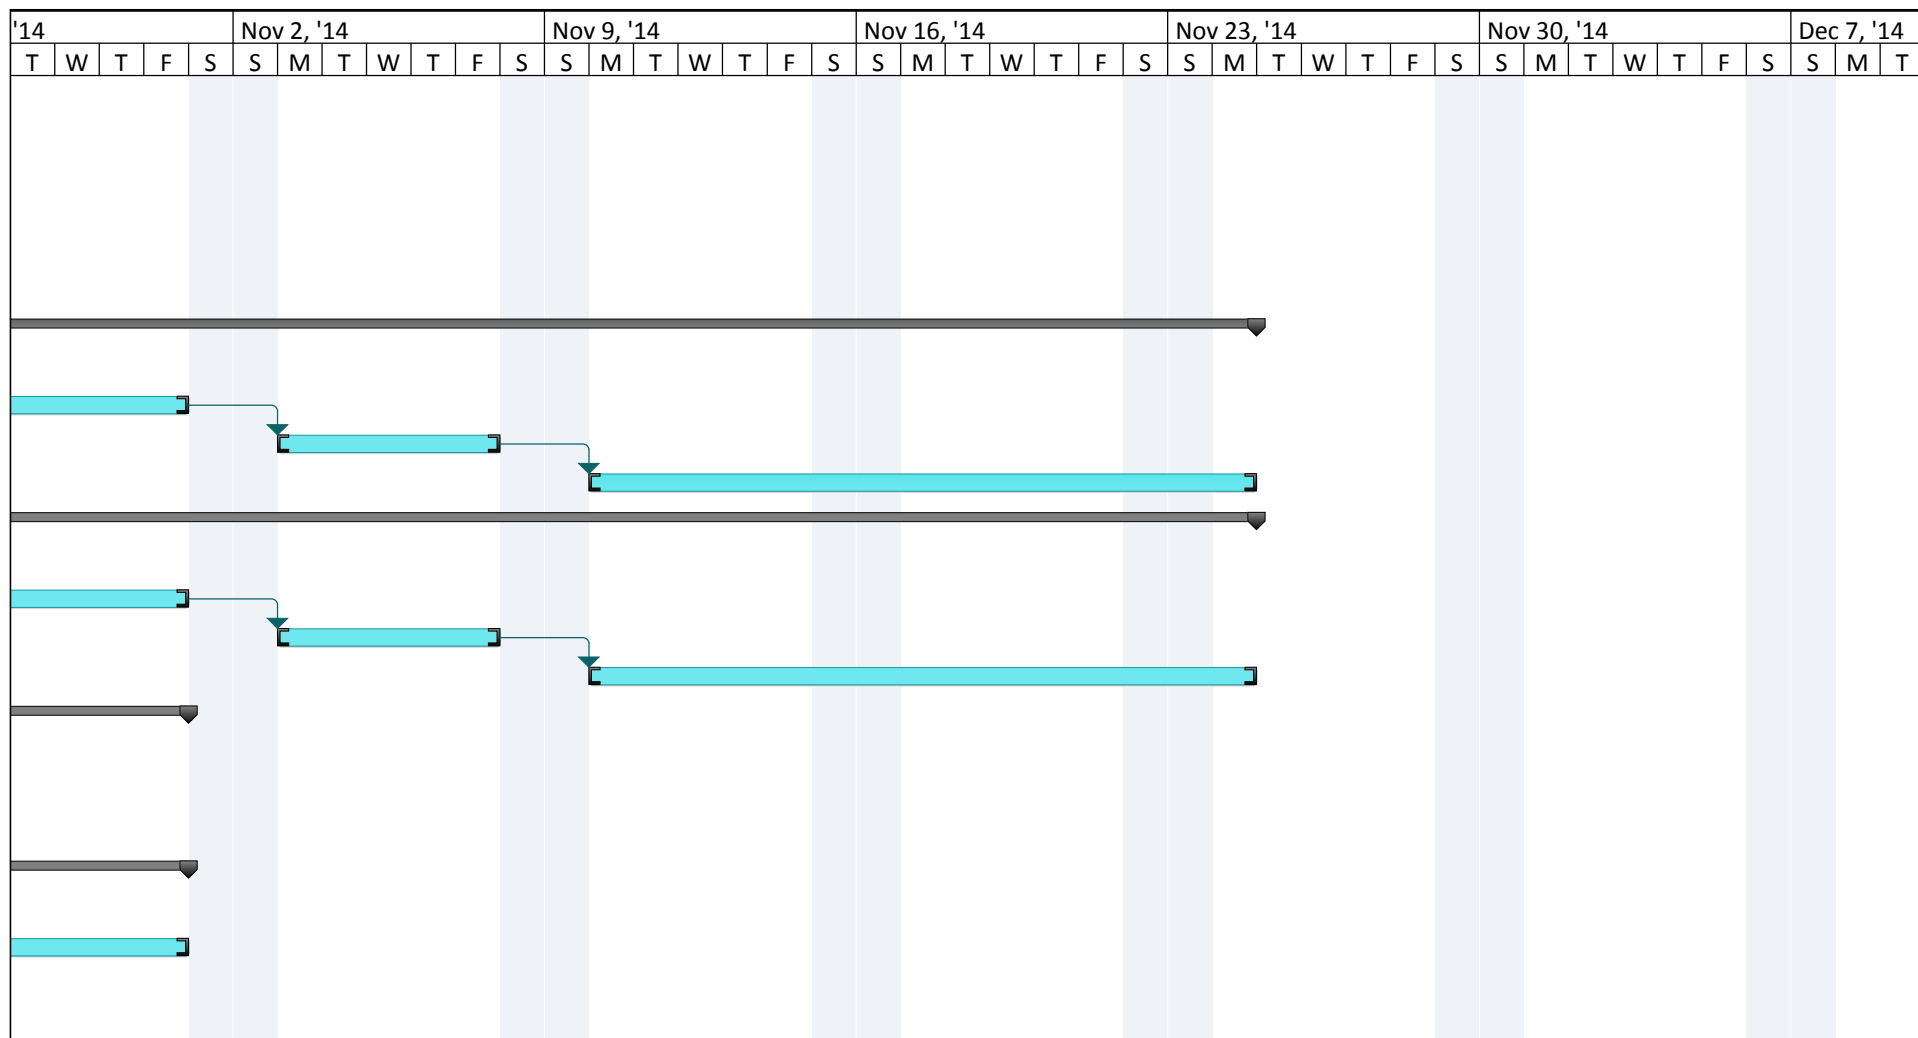

[illegible]

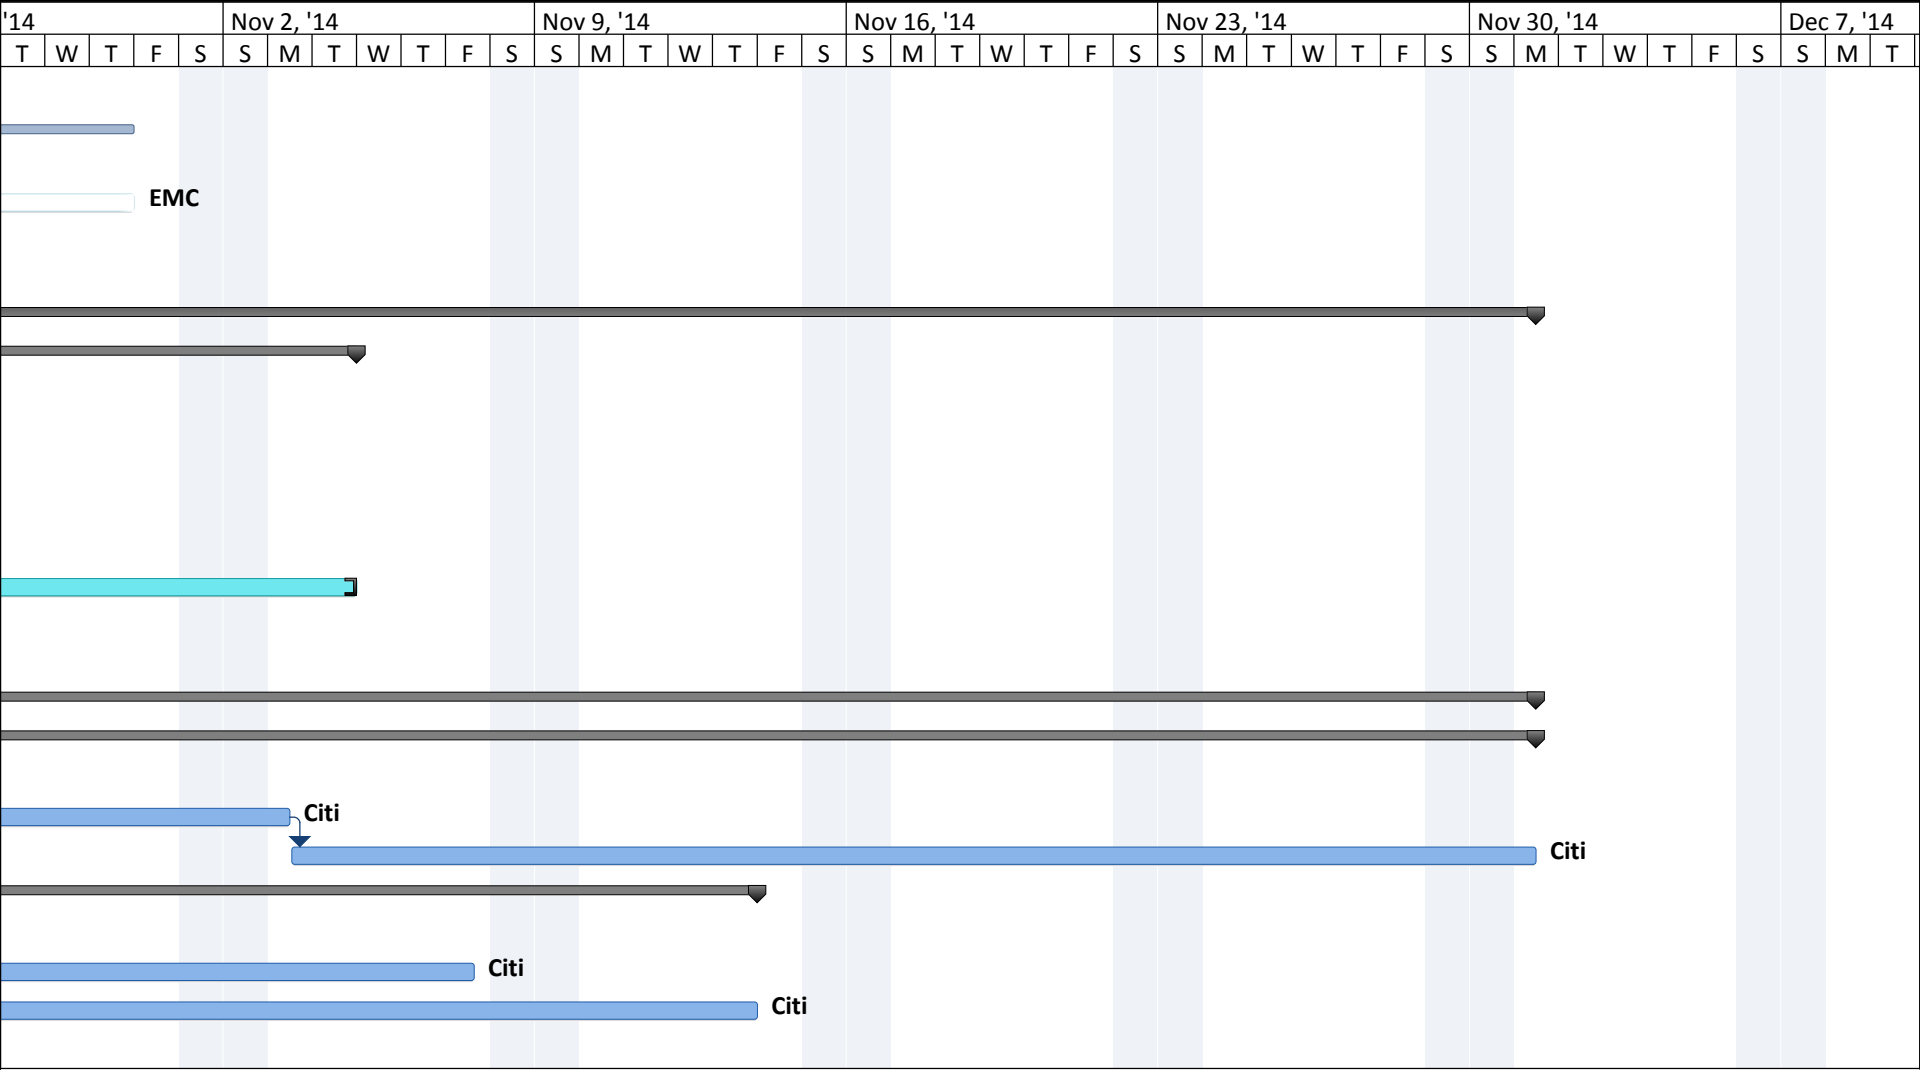

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

'14					Nov 2, '14								Nov 9, '14								Nov 16, '14								Nov 23, '14								Nov 30, '14								Dec 7, '14			
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T						

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

				Dec 14, '14								Dec 21, '14								Dec 28, '14								Jan 4, '15								Jan 11, '15								Jan 18, '15			
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W												

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

				Dec 14, '14								Dec 21, '14								Dec 28, '14								Jan 4, '15								Jan 11, '15								Jan 18, '15			
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W												

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


Deadline

Progress

[illegible]

				Dec 14, '14								Dec 21, '14								Dec 28, '14								Jan 4, '15								Jan 11, '15								Jan 18, '15			
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W												
										EMC																																					

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

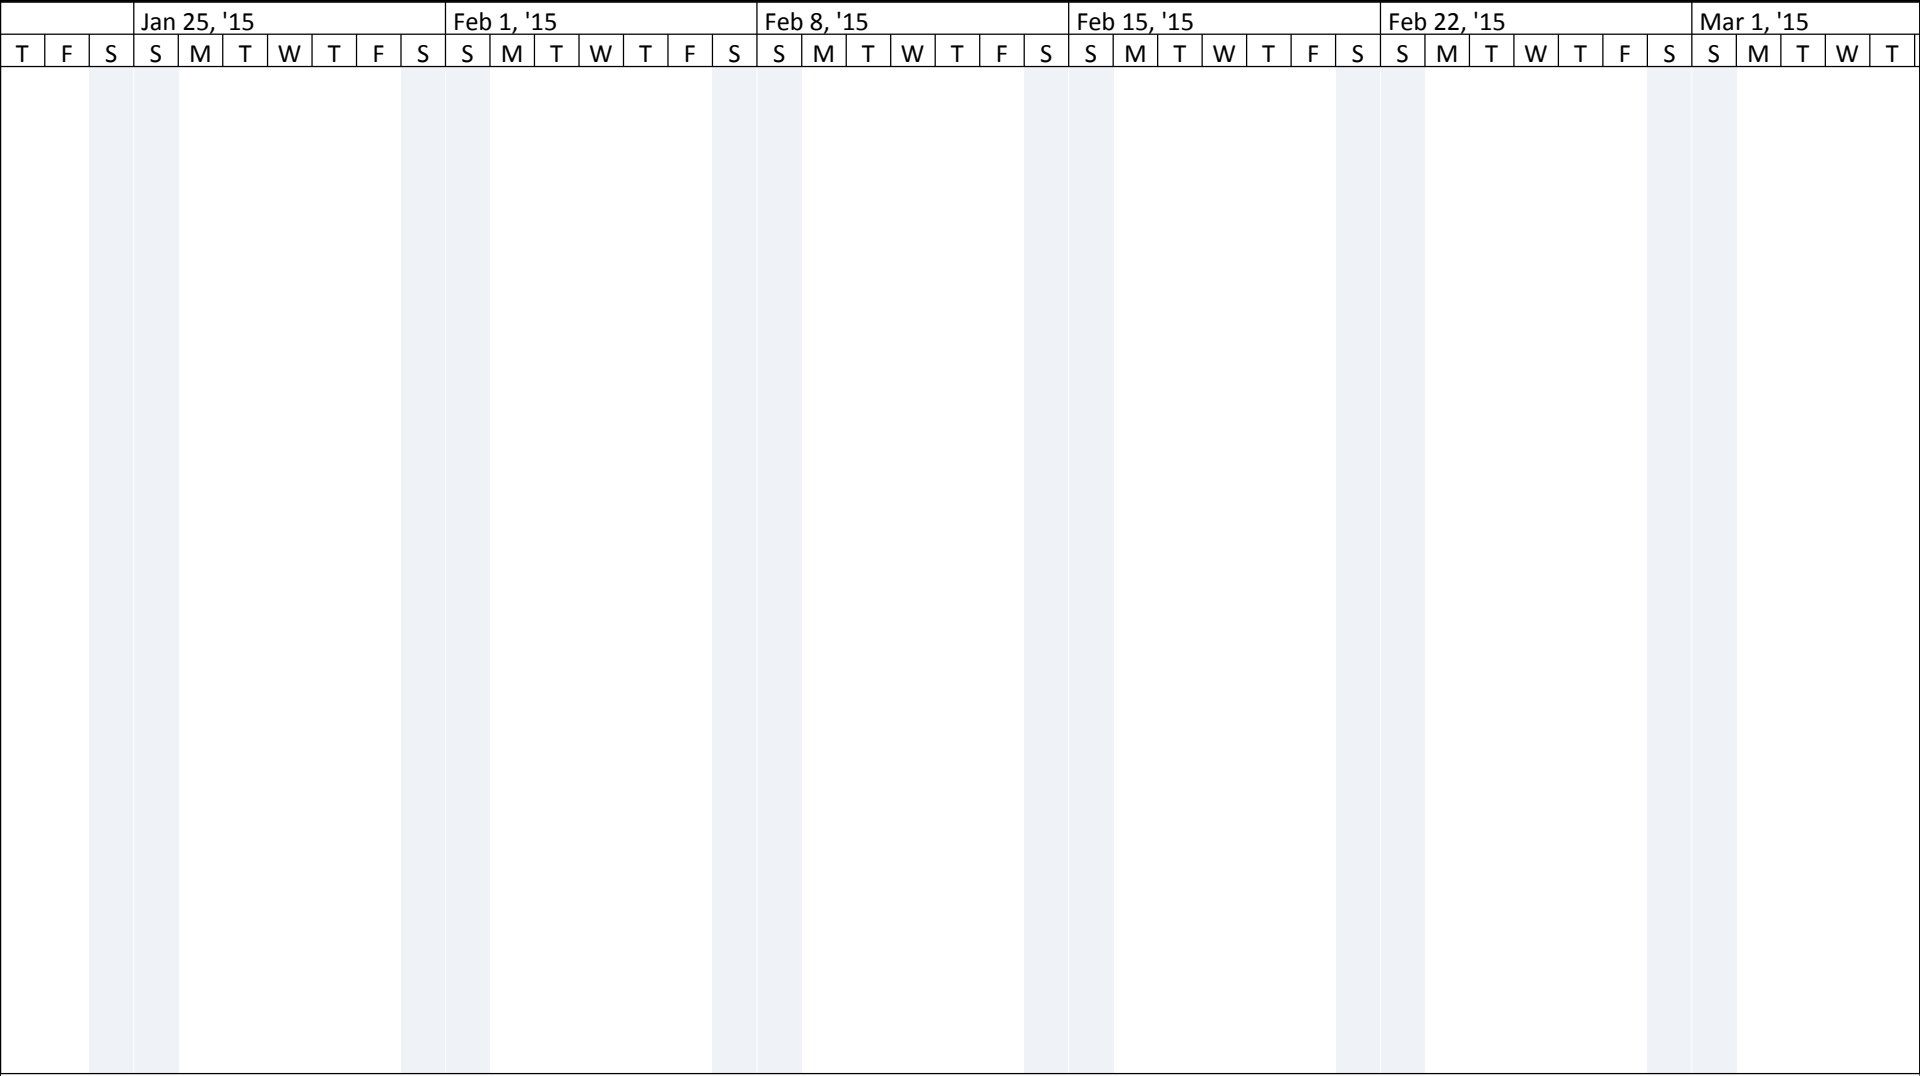

Project: SRM Deployment Project
Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only

Deadline

Progress

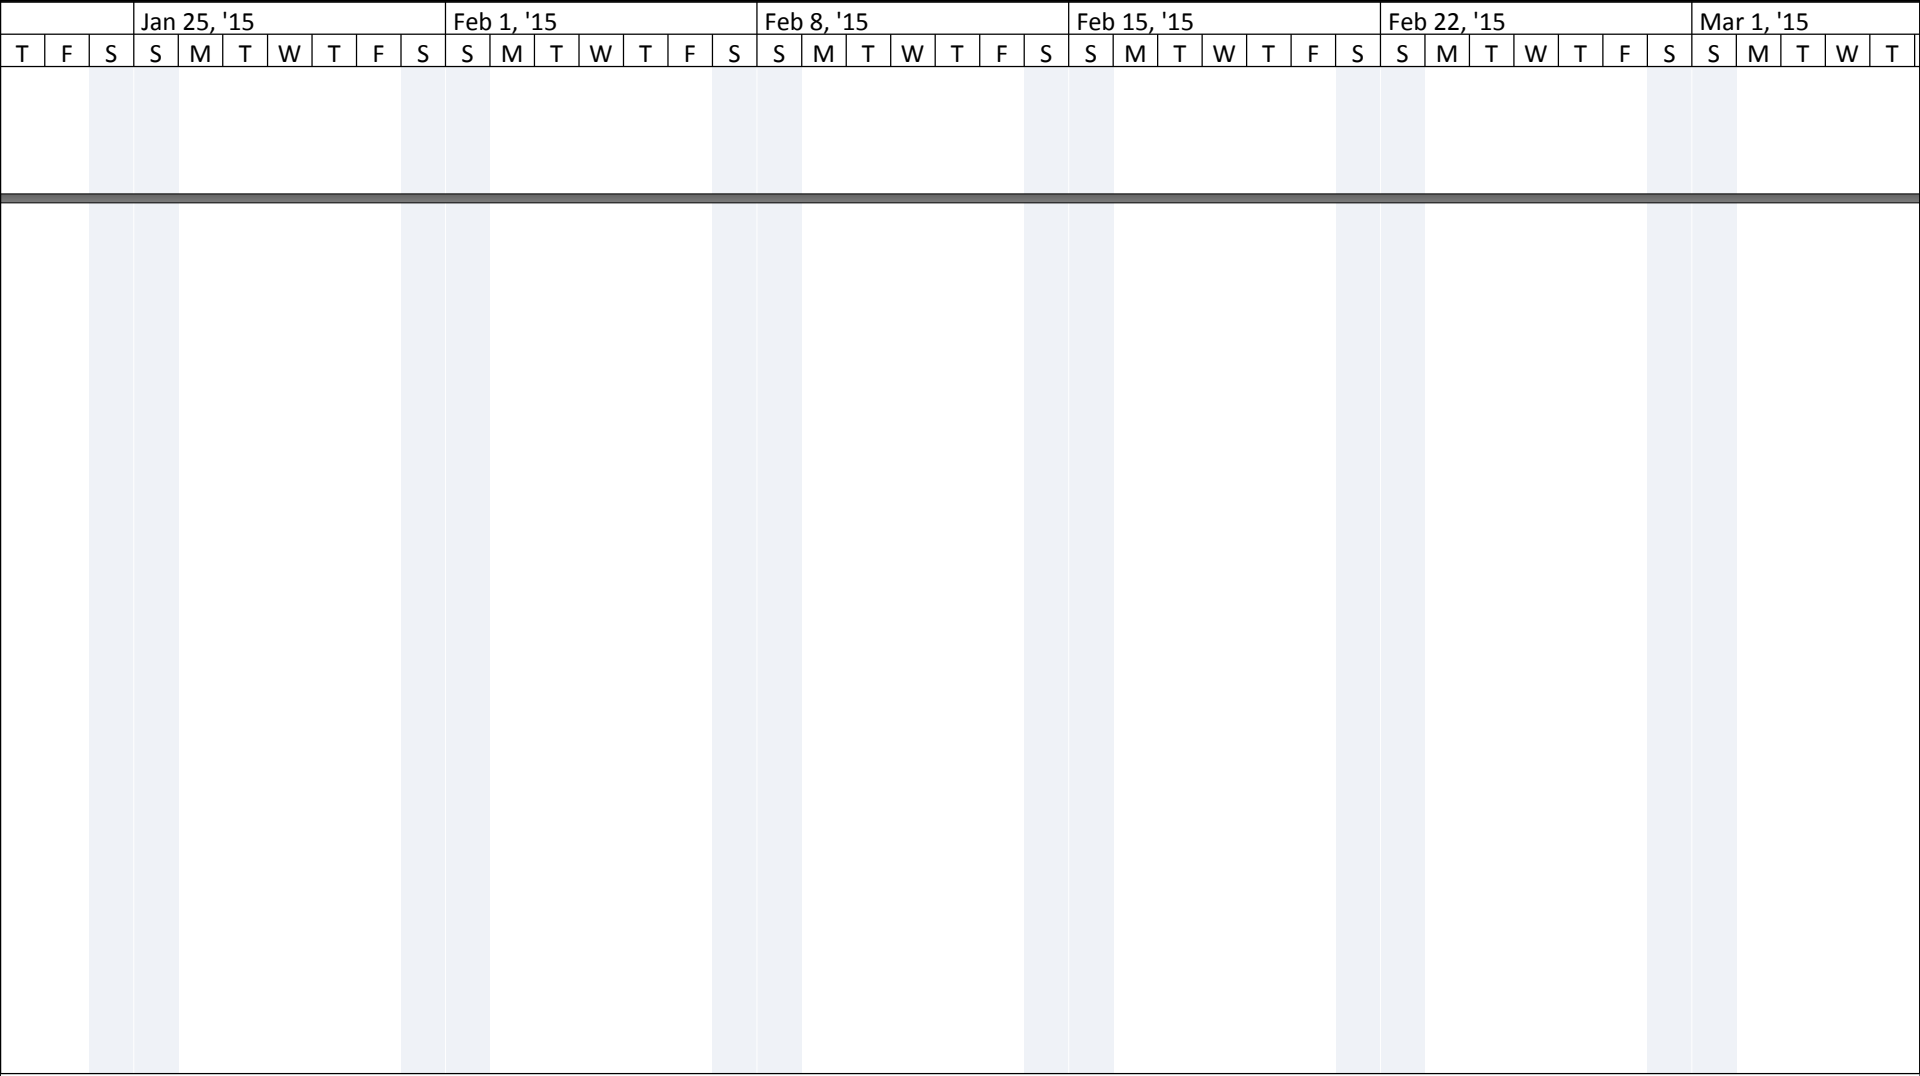

Project: SRM Deployment Project
Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only

Deadline

Progress

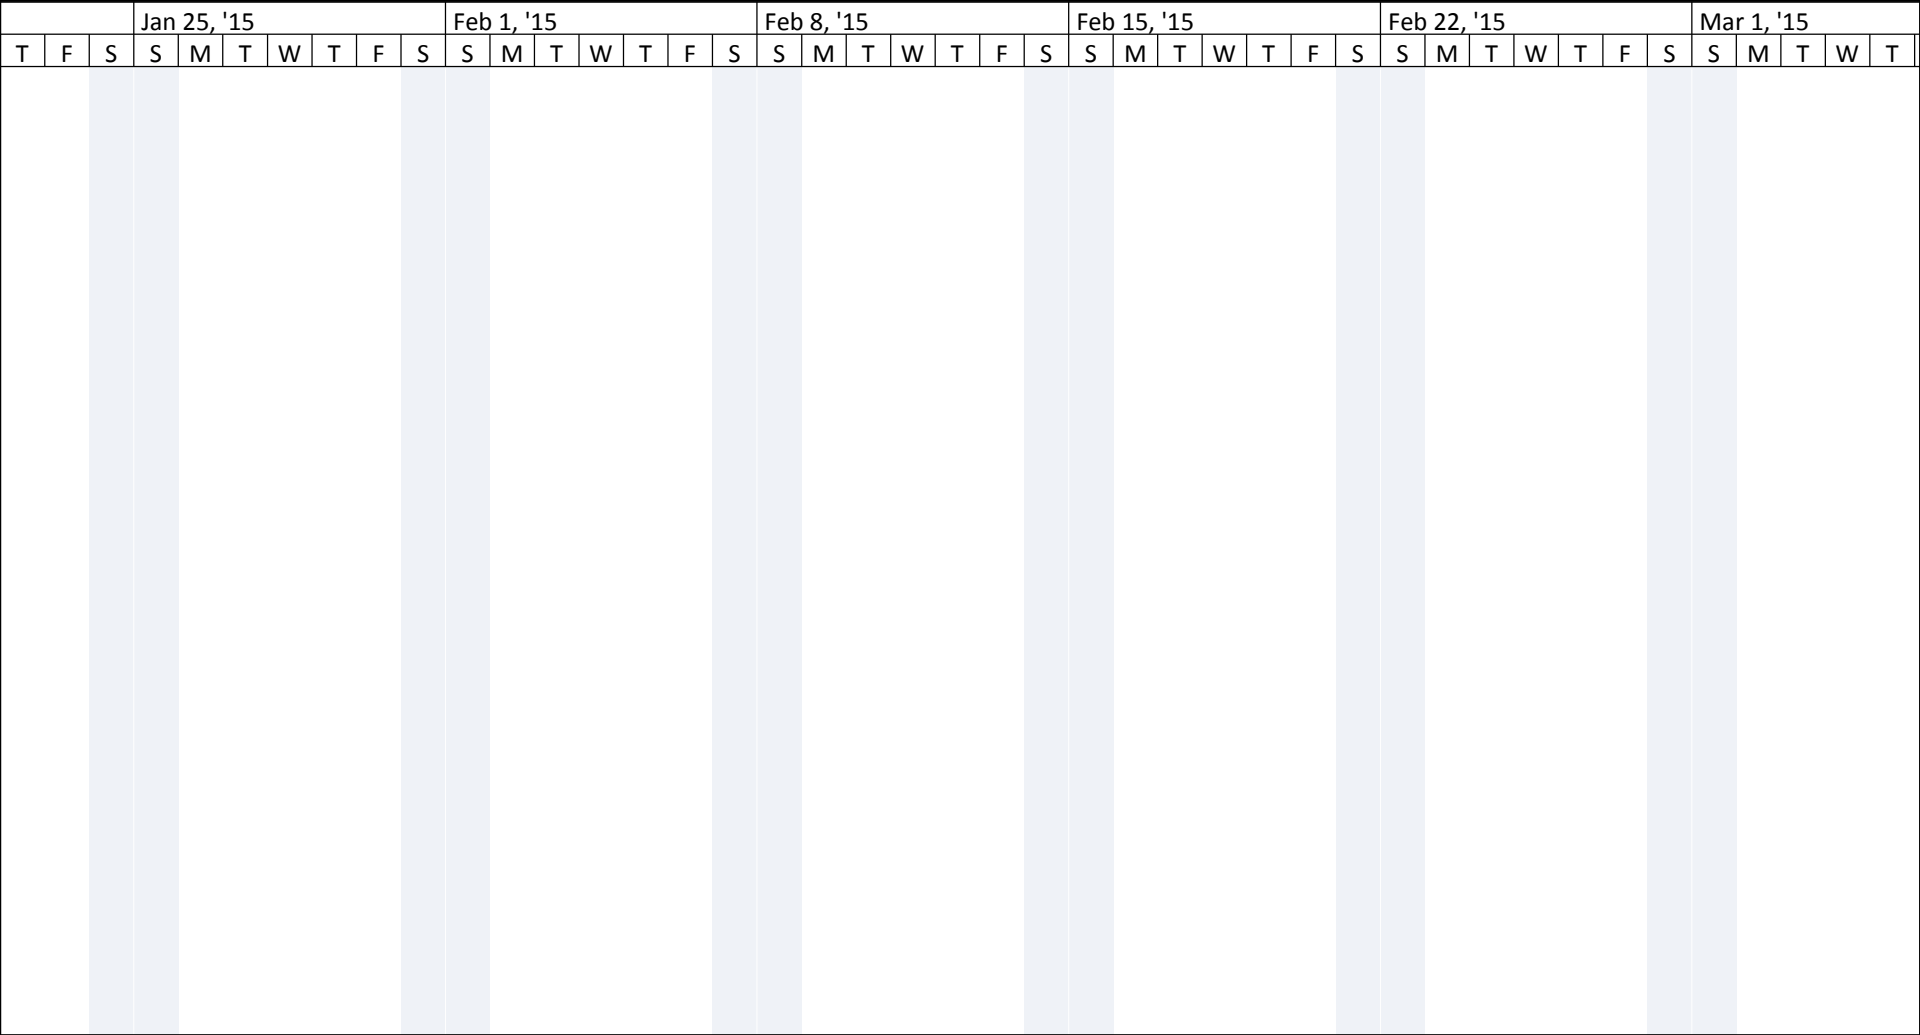

Project: SRM Deployment Project
Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

			Jan 25, '15					Feb 1, '15					Feb 8, '15					Feb 15, '15					Feb 22, '15					Mar 1, '15							
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T
</																																			

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
Page 95						

			Jan 25, '15								Feb 1, '15								Feb 8, '15								Feb 15, '15								Feb 22, '15								Mar 1, '15							
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T															

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

			Jan 25, '15							Feb 1, '15							Feb 8, '15							Feb 15, '15							Feb 22, '15							Mar 1, '15						
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T									

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

			Jan 25, '15							Feb 1, '15							Feb 8, '15							Feb 15, '15							Feb 22, '15							Mar 1, '15					
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	



Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

		Mar 8, '15							Mar 15, '15							Mar 22, '15							Mar 29, '15							Apr 5, '15							Apr 12, '15						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

		Mar 8, '15							Mar 15, '15							Mar 22, '15							Mar 29, '15							Apr 5, '15							Apr 12, '15						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F								

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only


Finish-only

Deadline

Progress

		Mar 8, '15							Mar 15, '15							Mar 22, '15							Mar 29, '15							Apr 5, '15							Apr 12, '15						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

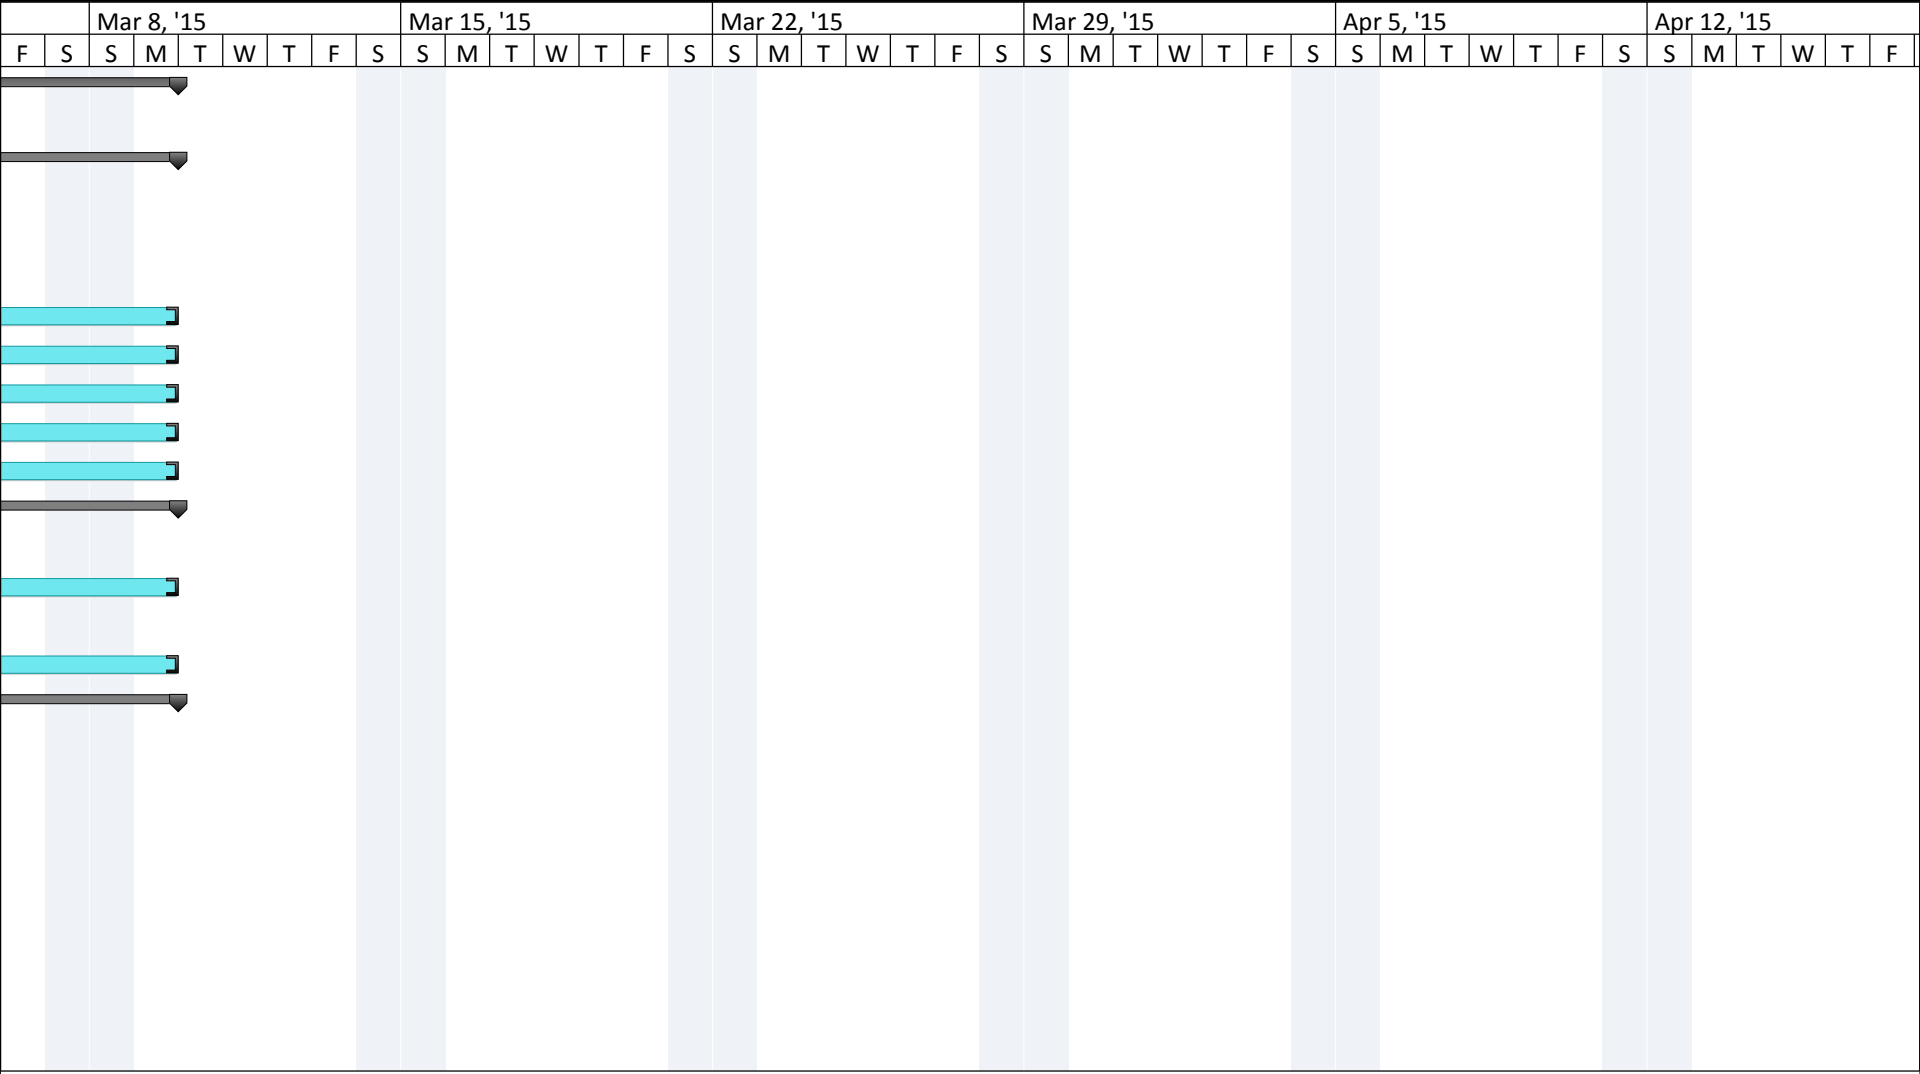

Project: SRM Deployment Project
Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

[illegible]

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

		Mar 8, '15							Mar 15, '15							Mar 22, '15							Mar 29, '15							Apr 5, '15							Apr 12, '15						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

		Mar 8, '15								Mar 15, '15								Mar 22, '15								Mar 29, '15								Apr 5, '15								Apr 12, '15							
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F							



Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

Apr 19, '15								Apr 26, '15								May 3, '15								May 10, '15								May 17, '15								May 24, '15							
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S					



Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

May 31, '15							Jun 7, '15							Jun 14, '15							Jun 21, '15							Jun 28, '15							Jul 5, '15							Jul 12, '15	
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S								

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

May 31, '15							Jun 7, '15							Jun 14, '15							Jun 21, '15							Jun 28, '15							Jul 5, '15							Jul 12, '15	
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S								

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only

Deadline

Progress

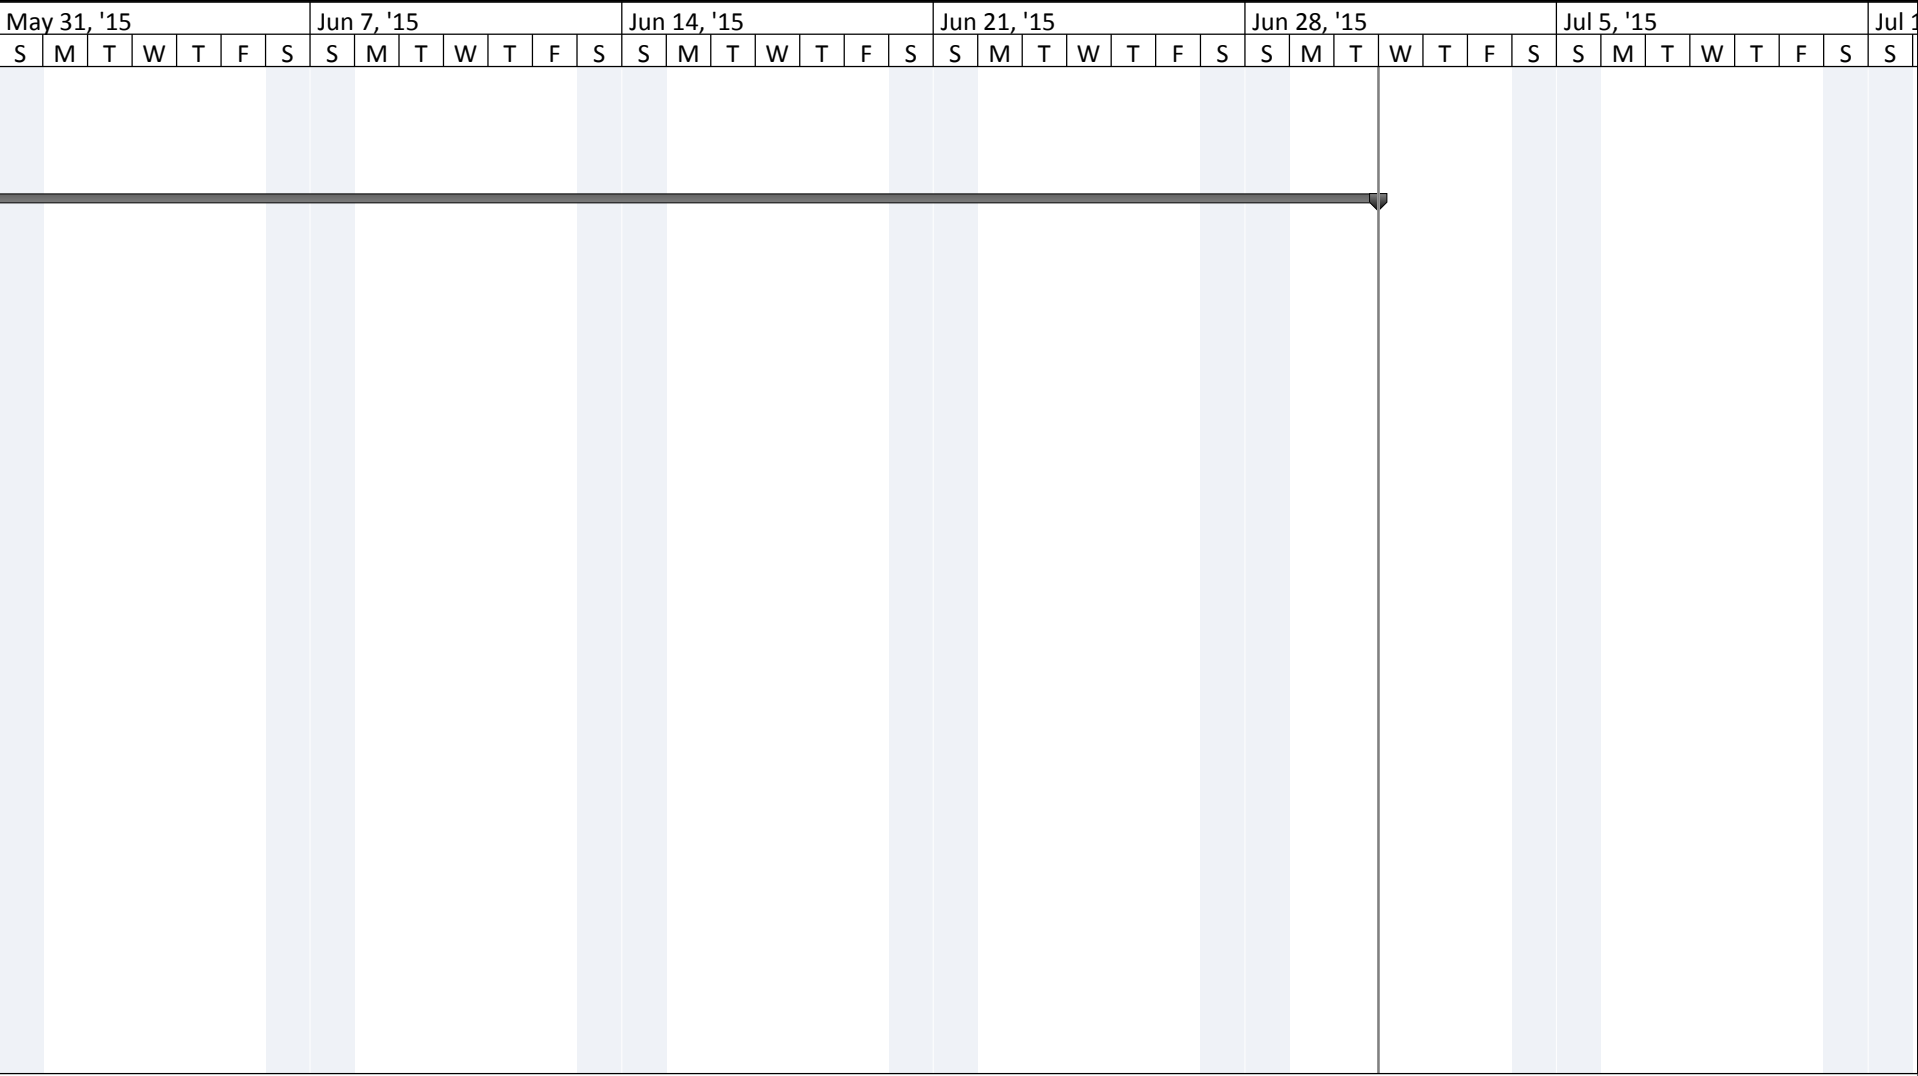

Project: SRM Deployment Project
Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

May 31, '15							Jun 7, '15							Jun 14, '15							Jun 21, '15							Jun 28, '15							Jul 5, '15							Jul 12, '15
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S							

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

May 31, '15							Jun 7, '15							Jun 14, '15							Jun 21, '15							Jun 28, '15							Jul 5, '15							Jul 12, '15	
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S								

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]

Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

May 31, '15							Jun 7, '15							Jun 14, '15							Jun 21, '15							Jun 28, '15							Jul 5, '15							Jul 12, '15	
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S								

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

May 31, '15							Jun 7, '15							Jun 14, '15							Jun 21, '15							Jun 28, '15							Jul 5, '15							Jul 12, '15	
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S								

Project: SRM Deployment Project

Date: Mon 10/27/14

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

May 31, '15							Jun 7, '15							Jun 14, '15							Jun 21, '15							Jun 28, '15							Jul 5, '15							Jul 12, '15	
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	



Project: SRM Deployment Project Date: Mon 10/27/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
